



| ID | Task Name   | Duration          | Start              | Finish             | Predecessors | /06 |   |   |   |   |   |   | 3/6/06 |  |
|----|---|-------------------|--------------------|--------------------|--------------|-----|---|---|---|---|---|---|--------|--|
|    |   |                   |                    |                    |              | T   | W | T | F | S | S | M | T      |  |
| 1  | Nursing & Patient Care Documentation System             | 325 days?         | Wed 3/1/06         | Thu 1/31/08        |              |     |   |   |   |   |   |   |        |  |
| 2  | <b>Scope</b>  | <b>4.58 days</b>  | <b>Wed 3/1/06</b>  | <b>Tue 3/7/06</b>  |              |     |   |   |   |   |   |   |        |  |
| 3  | Determine project scope                                 | 2 hrs             | Wed 3/1/06         | Wed 3/1/06         |              |     |   |   |   |   |   |   |        |  |
| 4  | Secure project sponsorship/Define Governance            | 1 day             | Wed 3/1/06         | Thu 3/2/06         | 3            |     |   |   |   |   |   |   |        |  |
| 5  | Define preliminary resources                            | 1 day             | Wed 3/1/06         | Thu 3/2/06         | 4SS          |     |   |   |   |   |   |   |        |  |
| 6  | Secure core resources                                   | 0.33 days         | Thu 3/2/06         | Thu 3/2/06         | 5            |     |   |   |   |   |   |   |        |  |
| 7  | Develop Project Risk Management Plan                    | 3 days            | Thu 3/2/06         | Tue 3/7/06         | 6            |     |   |   |   |   |   |   |        |  |
| 8  | Scope complete  | 0 days            | Tue 3/7/06         | Tue 3/7/06         | 7            |     |   |   |   |   |   |   |        |  |
| 9  | <b>Analysis/Software Requirements</b>                   | <b>25.5 days?</b> | <b>Tue 3/7/06</b>  | <b>Wed 4/12/06</b> |              |     |   |   |   |   |   |   |        |  |
| 10 | Conduct needs analysis                                  | 5 days            | Tue 3/7/06         | Tue 3/14/06        | 8            |     |   |   |   |   |   |   |        |  |
| 11 | Draft preliminary software requirements                 | 3 days            | Tue 3/14/06        | Fri 3/17/06        | 10           |     |   |   |   |   |   |   |        |  |
| 12 | Conduct Gap Analysis/Formulate Strategy                 | 1 day?            | Fri 3/17/06        | Mon 3/20/06        | 11           |     |   |   |   |   |   |   |        |  |
| 13 | Develop preliminary budget                              | 2 days            | Mon 3/20/06        | Wed 3/22/06        | 12           |     |   |   |   |   |   |   |        |  |
| 14 | Review software specifications/budget with team         | 8 hrs             | Wed 3/22/06        | Thu 3/23/06        | 13           |     |   |   |   |   |   |   |        |  |
| 15 | Incorporate feedback on software specifications         | 2 days            | Thu 3/23/06        | Mon 3/27/06        | 14           |     |   |   |   |   |   |   |        |  |
| 16 | Sign-off on Nursing Procedural Changes                  | 1 day             | Mon 3/27/06        | Tue 3/28/06        | 15           |     |   |   |   |   |   |   |        |  |
| 17 | Develop/negotiate vendor delivery timeline              | 1 day             | Tue 3/28/06        | Wed 3/29/06        | 16           |     |   |   |   |   |   |   |        |  |
| 18 | Obtain approvals to proceed (concept, timeline, budget) | 8 hrs             | Wed 3/29/06        | Thu 3/30/06        | 17           |     |   |   |   |   |   |   |        |  |
| 19 | Secure required resources                               | 7 days            | Thu 3/30/06        | Mon 4/10/06        | 18           |     |   |   |   |   |   |   |        |  |
| 20 | Analysis complete                                       | 1 day             | Mon 4/10/06        | Wed 4/12/06        | 19           |     |   |   |   |   |   |   |        |  |
| 21 | <b>Design/Configuration Software</b>                    | <b>70 days?</b>   | <b>Wed 4/12/06</b> | <b>Wed 7/19/06</b> |              |     |   |   |   |   |   |   |        |  |
| 22 | Review preliminary software specifications              | 2 days            | Wed 4/12/06        | Fri 4/14/06        | 20           |     |   |   |   |   |   |   |        |  |
| 23 | Develop functional specifications                       | 15 days           | Fri 4/14/06        | Fri 5/5/06         | 22           |     |   |   |   |   |   |   |        |  |
| 24 | Develop prototype based on functional specifications    | 4 days            | Fri 5/5/06         | Thu 5/11/06        | 23           |     |   |   |   |   |   |   |        |  |
| 25 | Review functional specifications                        | 2 days            | Thu 5/11/06        | Mon 5/15/06        | 24           |     |   |   |   |   |   |   |        |  |
| 26 | Incorporate feedback into functional specifications     | 2 days            | Mon 5/15/06        | Wed 5/17/06        | 25           |     |   |   |   |   |   |   |        |  |
| 27 | Obtain approval to proceed with configuration           | 8 hrs             | Wed 5/17/06        | Thu 5/18/06        | 26           |     |   |   |   |   |   |   |        |  |
| 28 | Design complete   | 0 days            | Thu 5/18/06        | Thu 5/18/06        | 27           |     |   |   |   |   |   |   |        |  |
| 29 | <b>Design/Configuration Hardware</b>                    | 32 days           | Thu 5/18/06        | Mon 7/3/06         | 28           |     |   |   |   |   |   |   |        |  |
| 30 | Review preliminary hardware specifications by unit      | 10 days           | Mon 7/3/06         | Mon 7/17/06        | 29           |     |   |   |   |   |   |   |        |  |
| 31 | Identify additional hardware needs by unit              | 10 days           | Mon 7/3/06         | Mon 7/17/06        | 30SS         |     |   |   |   |   |   |   |        |  |
| 32 | Ceiling pulls - each unit                               | 1 day?            | Mon 7/17/06        | Tue 7/18/06        | 31           |     |   |   |   |   |   |   |        |  |





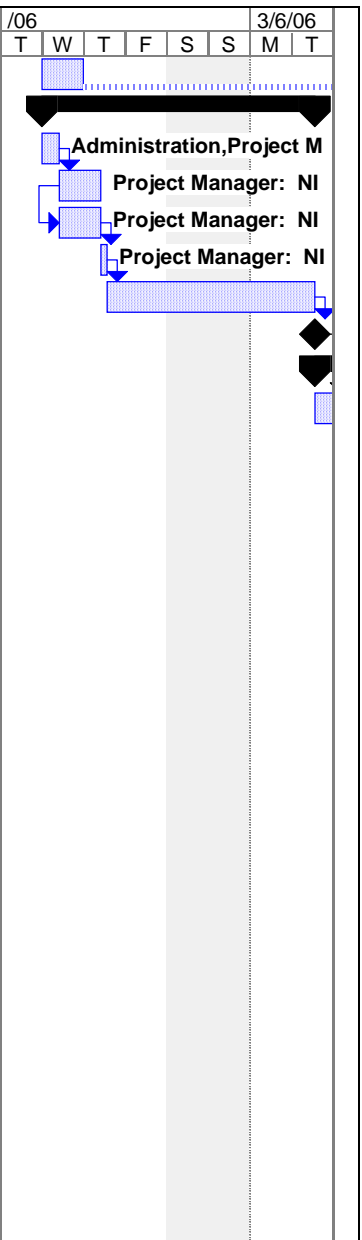






|  |          |  |                 |  |                    |  |
|--|----------|--|-----------------|--|--------------------|--|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |

| ID | Task Name   | Duration          | Start              | Finish              | Predecessors | /06 |   |   |   |   |   |   | 3/6/06 |  |
|----|---|-------------------|--------------------|---------------------|--------------|-----|---|---|---|---|---|---|--------|--|
|    |   |                   |                    |                     |              | T   | W | T | F | S | S | M | T      |  |
| 33 | Obtain approval to proceed with hardware purchase           | 1 day?            | Tue 7/18/06        | Wed 7/19/06         | 32           |     |   |   |   |   |   |   |        |  |
| 34 | Design complete   | 0 days            | Wed 7/19/06        | Wed 7/19/06         | 33           |     |   |   |   |   |   |   |        |  |
| 35 | <b>Development of application</b>                           | <b>7.92 days</b>  | <b>Wed 7/19/06</b> | <b>Fri 7/28/06</b>  |              |     |   |   |   |   |   |   |        |  |
| 36 | Review functional specifications                            | 1 day             | Wed 7/19/06        | Thu 7/20/06         | 34           |     |   |   |   |   |   |   |        |  |
| 37 | Identify modular/tiered design parameters                   | 0.33 days         | Thu 7/20/06        | Thu 7/20/06         | 36           |     |   |   |   |   |   |   |        |  |
| 38 | Assign development staff                                    | 0.33 days         | Thu 7/20/06        | Thu 7/20/06         | 37           |     |   |   |   |   |   |   |        |  |
| 39 | Develop code  | 5 days            | Thu 7/20/06        | Thu 7/27/06         | 38           |     |   |   |   |   |   |   |        |  |
| 40 | Developer testing (primary debugging)                       | 5 days            | Mon 7/24/06        | Fri 7/28/06         | 39FS-75%     |     |   |   |   |   |   |   |        |  |
| 41 | Development complete  | 0 days            | Fri 7/28/06        | Fri 7/28/06         | 40           |     |   |   |   |   |   |   |        |  |
| 42 | <b>Development of interfaces</b>                            | <b>114 days?</b>  | <b>Wed 3/1/06</b>  | <b>Mon 8/7/06</b>   |              |     |   |   |   |   |   |   |        |  |
| 43 | Review functional specifications                            | 61 days           | Wed 3/1/06         | Wed 5/24/06         |              |     |   |   |   |   |   |   |        |  |
| 44 | Identify modular/tiered design parameters                   | 61 days           | Wed 3/1/06         | Wed 5/24/06         | 43SS         |     |   |   |   |   |   |   |        |  |
| 45 | Assign development staff                                    | 1 day?            | Thu 5/25/06        | Thu 5/25/06         | 44           |     |   |   |   |   |   |   |        |  |
| 46 | Develop code  | 32 days           | Fri 5/26/06        | Mon 7/10/06         | 45           |     |   |   |   |   |   |   |        |  |
| 47 | Developer testing (primary debugging)                       | 20 days           | Tue 7/11/06        | Mon 8/7/06          | 46           |     |   |   |   |   |   |   |        |  |
| 48 | Development complete  | 0 days            | Mon 8/7/06         | Mon 8/7/06          | 47           |     |   |   |   |   |   |   |        |  |
| 49 | <b>Development of Reports</b>                               | <b>113 days?</b>  | <b>Tue 7/11/06</b> | <b>Thu 12/14/06</b> | <b>47SS</b>  |     |   |   |   |   |   |   |        |  |
| 50 | Review functional specifications                            | 61 days           | Tue 7/11/06        | Tue 10/3/06         |              |     |   |   |   |   |   |   |        |  |
| 51 | Identify modular/tiered design parameters                   | 61 days           | Tue 7/11/06        | Tue 10/3/06         | 50SS         |     |   |   |   |   |   |   |        |  |
| 52 | Assign development staff                                    | 1 day?            | Wed 10/4/06        | Wed 10/4/06         | 51           |     |   |   |   |   |   |   |        |  |
| 53 | Develop code  | 32 days           | Wed 10/4/06        | Thu 11/16/06        | 51           |     |   |   |   |   |   |   |        |  |
| 54 | Developer testing (primary debugging)                       | 20 days           | Fri 11/17/06       | Thu 12/14/06        | 53           |     |   |   |   |   |   |   |        |  |
| 55 | Development complete  | 0 days            | Thu 12/14/06       | Thu 12/14/06        | 54           |     |   |   |   |   |   |   |        |  |
| 56 | <b>Testing</b>  | <b>62.33 days</b> | <b>Thu 5/18/06</b> | <b>Mon 8/14/06</b>  |              |     |   |   |   |   |   |   |        |  |
| 57 | Develop unit test plans using product specifications        | 4 days            | Thu 5/18/06        | Wed 5/24/06         | 28           |     |   |   |   |   |   |   |        |  |
| 58 | Develop integration test plans using product specifications | 1.33 days         | Thu 5/18/06        | Fri 5/19/06         | 28           |     |   |   |   |   |   |   |        |  |
| 59 | <b>Unit Testing</b>   | <b>3.75 days</b>  | <b>Mon 7/31/06</b> | <b>Thu 8/3/06</b>   |              |     |   |   |   |   |   |   |        |  |
| 60 | Review modular code/determine units for testing             | 1.25 days         | Mon 7/31/06        | Tue 8/1/06          | 57,41        |     |   |   |   |   |   |   |        |  |
| 61 | Test component modules to product specifications            | 0.5 days          | Tue 8/1/06         | Tue 8/1/06          | 41,60        |     |   |   |   |   |   |   |        |  |
| 62 | Identify anomalies to product specifications                | 0.75 days         | Tue 8/1/06         | Wed 8/2/06          | 61           |     |   |   |   |   |   |   |        |  |
| 63 | Modify code   | 0.75 days         | Wed 8/2/06         | Thu 8/3/06          | 62           |     |   |   |   |   |   |   |        |  |
| 64 | Re-test modified code                                       | 0.5 days          | Thu 8/3/06         | Thu 8/3/06          | 63           |     |   |   |   |   |   |   |        |  |












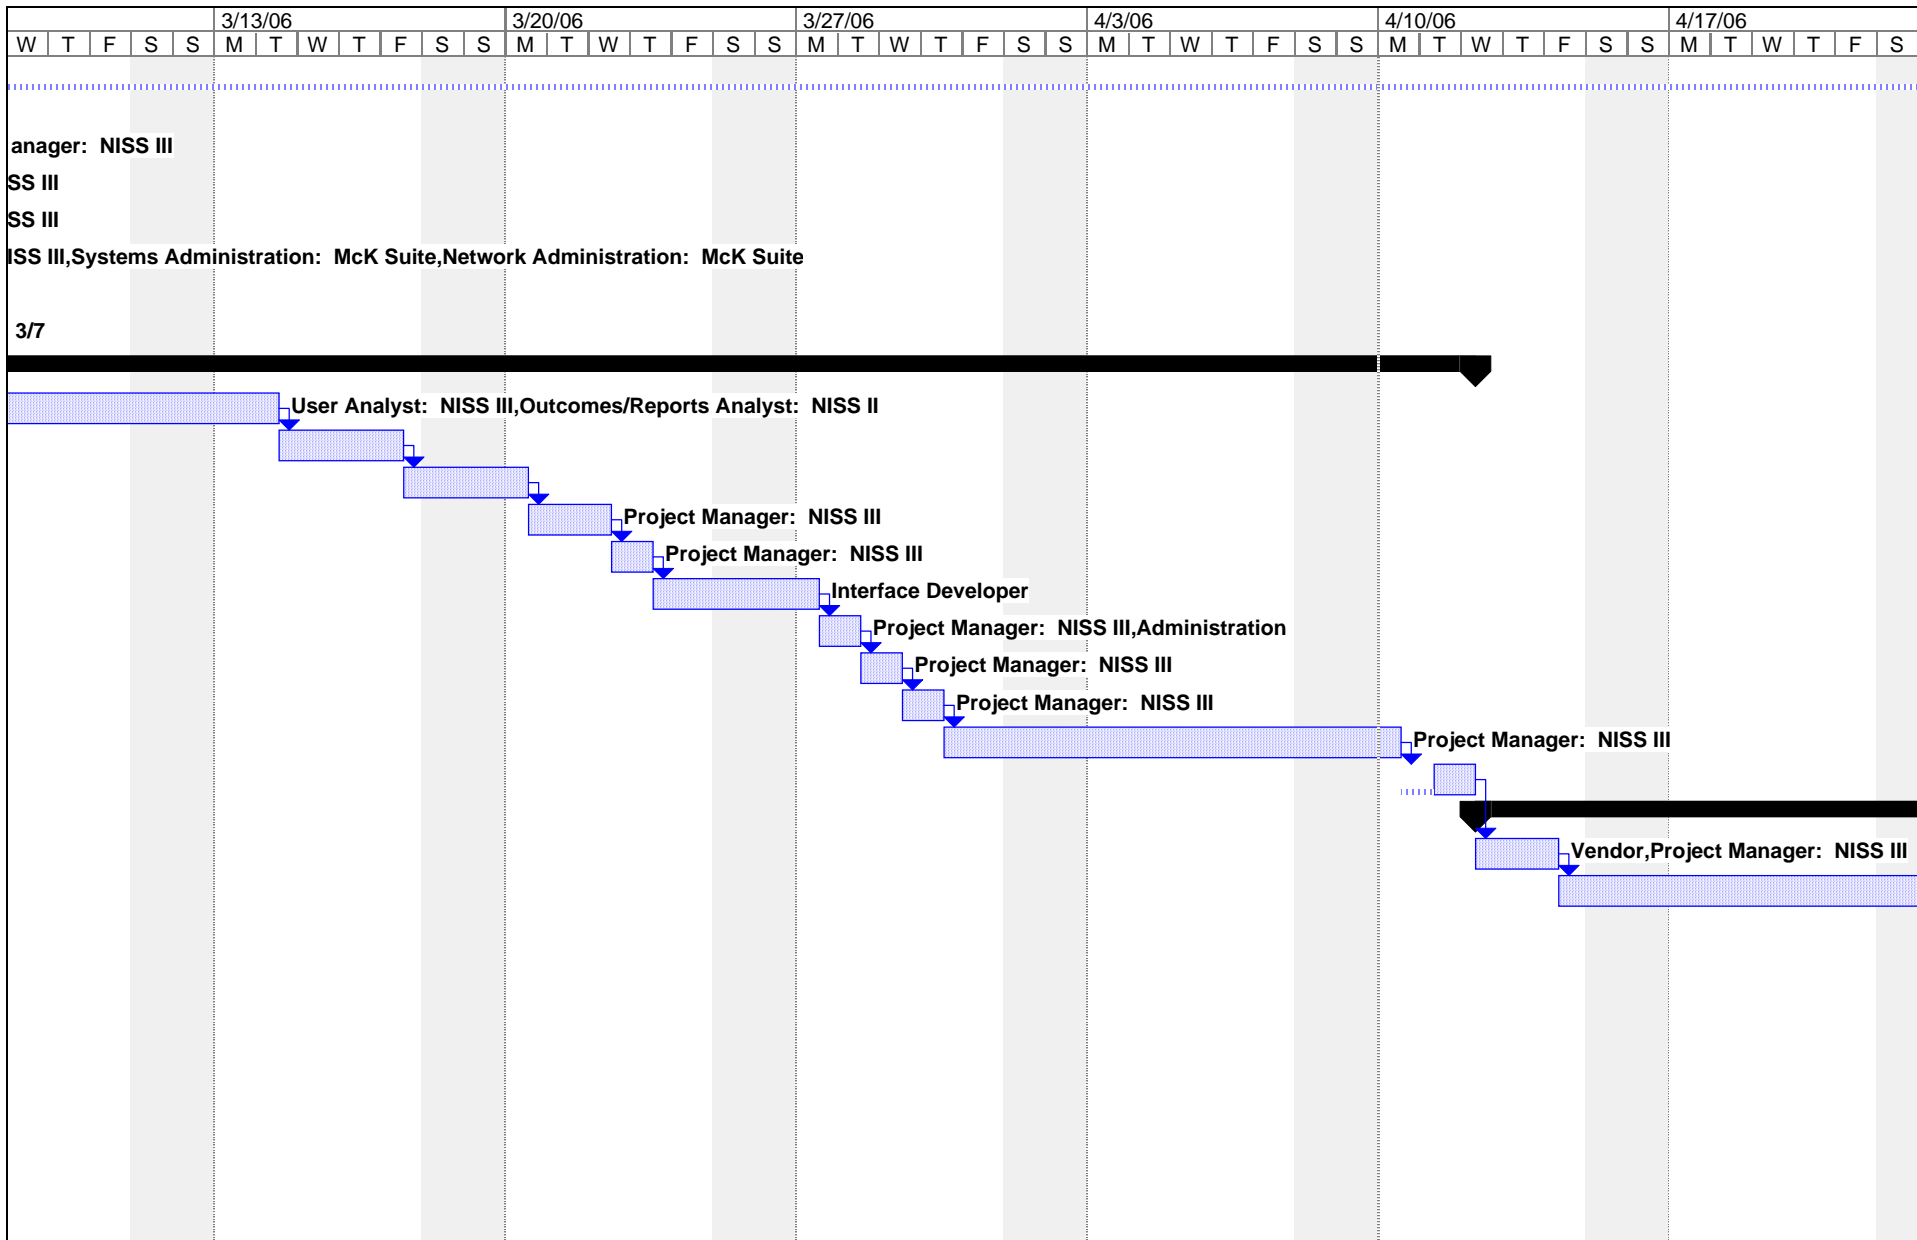
|  |          |  |                 |  |                    |  |
|--|----------|--|-----------------|--|--------------------|--|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |

| ID | Task Name   | Duration           | Start              | Finish             | Predecessors | /06 |   |   |   |   |   |   | 3/6/06 |  |
|----|---|--------------------|--------------------|--------------------|--------------|-----|---|---|---|---|---|---|--------|--|
|    |   |                    |                    |                    |              | T   | W | T | F | S | S | M | T      |  |
| 65 | Unit testing complete   | 0 days             | Thu 8/3/06         | Thu 8/3/06         | 64           |     |   |   |   |   |   |   |        |  |
| 66 | <b>Integration Testing</b>  | <b>6.67 days</b>   | <b>Thu 8/3/06</b>  | <b>Mon 8/14/06</b> |              |     |   |   |   |   |   |   |        |  |
| 67 | Test module integration   | 1.67 days          | Thu 8/3/06         | Mon 8/7/06         | 65           |     |   |   |   |   |   |   |        |  |
| 68 | Identify anomalies to specifications                                | 3 days             | Mon 8/7/06         | Thu 8/10/06        | 67           |     |   |   |   |   |   |   |        |  |
| 69 | Modify code   | 1 day              | Thu 8/10/06        | Fri 8/11/06        | 68           |     |   |   |   |   |   |   |        |  |
| 70 | Re-test modified code   | 1 day              | Fri 8/11/06        | Mon 8/14/06        | 69           |     |   |   |   |   |   |   |        |  |
| 71 | Integration testing complete  | 0 days             | Mon 8/14/06        | Mon 8/14/06        | 70           |     |   |   |   |   |   |   |        |  |
| 72 | <b>Training</b>   | <b>75.92 days?</b> | <b>Thu 5/18/06</b> | <b>Thu 8/31/06</b> |              |     |   |   |   |   |   |   |        |  |
| 73 | Develop training specifications for end users                       | 3 days             | Thu 5/18/06        | Tue 5/23/06        | 28           |     |   |   |   |   |   |   |        |  |
| 74 | Develop training specifications for helpdesk support staff          | 3 days             | Thu 5/18/06        | Tue 5/23/06        | 28           |     |   |   |   |   |   |   |        |  |
| 75 | Identify training delivery methodology (computer based training, cl | 2 days             | Thu 5/18/06        | Mon 5/22/06        | 28           |     |   |   |   |   |   |   |        |  |
| 76 | Develop training materials  | 3 wks              | Mon 7/31/06        | Fri 8/18/06        | 73,41,74,75  |     |   |   |   |   |   |   |        |  |
| 77 | Conduct training usability study                                    | 3 days             | Mon 8/21/06        | Wed 8/23/06        | 76           |     |   |   |   |   |   |   |        |  |
| 78 | Finalize training materials   | 3 days             | Thu 8/24/06        | Mon 8/28/06        | 77           |     |   |   |   |   |   |   |        |  |
| 79 | Develop training delivery mechanism                                 | 2 days             | Tue 8/29/06        | Wed 8/30/06        | 78           |     |   |   |   |   |   |   |        |  |
| 80 | <a href="#">Secure deployment resources</a>                         | 1 day?             | Thu 8/31/06        | Thu 8/31/06        | 79           |     |   |   |   |   |   |   |        |  |
| 81 | Training materials complete   | 0 days             | Thu 8/31/06        | Thu 8/31/06        | 80           |     |   |   |   |   |   |   |        |  |
| 82 | <b>Documentation</b>  | <b>63.17 days</b>  | <b>Thu 5/18/06</b> | <b>Tue 8/15/06</b> |              |     |   |   |   |   |   |   |        |  |
| 83 | Develop Help specification  | 3 days             | Thu 5/18/06        | Tue 5/23/06        | 28           |     |   |   |   |   |   |   |        |  |
| 84 | Develop Help system   | 2 wks              | Tue 7/25/06        | Tue 8/8/06         | 83,39FS-50%  |     |   |   |   |   |   |   |        |  |
| 85 | Review Help documentation   | 3 days             | Tue 8/8/06         | Fri 8/11/06        | 84           |     |   |   |   |   |   |   |        |  |
| 86 | Incorporate Help documentation feedback                             | 2 days             | Fri 8/11/06        | Tue 8/15/06        | 85           |     |   |   |   |   |   |   |        |  |
| 87 | Develop user manuals specifications                                 | 1.33 days          | Thu 5/18/06        | Fri 5/19/06        | 28           |     |   |   |   |   |   |   |        |  |
| 88 | Develop user manuals  | 1 wk               | Tue 7/25/06        | Tue 8/1/06         | 87,39FS-50%  |     |   |   |   |   |   |   |        |  |
| 89 | Review all user documentation                                       | 3 days             | Tue 8/1/06         | Fri 8/4/06         | 88           |     |   |   |   |   |   |   |        |  |
| 90 | Incorporate user documentation feedback                             | 2 days             | Fri 8/4/06         | Tue 8/8/06         | 89           |     |   |   |   |   |   |   |        |  |
| 91 | Documentation complete  | 0 days             | Tue 8/15/06        | Tue 8/15/06        | 90,86        |     |   |   |   |   |   |   |        |  |
| 92 | <b>Phased Implementation</b>  | <b>370 days</b>    | <b>Fri 9/1/06</b>  | <b>Thu 1/31/08</b> |              |     |   |   |   |   |   |   |        |  |
| 93 | Determine final deployment strategy                                 | 2 days             | Fri 9/1/06         | Mon 9/4/06         |              |     |   |   |   |   |   |   |        |  |
| 94 | Meet with Nurse Manager to coordinate implementation plans          | 2 hrs              | Tue 9/5/06         | Tue 9/5/06         | 93           |     |   |   |   |   |   |   |        |  |
| 95 | Install Hardware on target unit(s)                                  | 5 days             | Tue 9/5/06         | Tue 9/12/06        | 94           |     |   |   |   |   |   |   |        |  |
| 96 | Install software on target unit(s)                                  | 3 days             | Tue 9/12/06        | Fri 9/15/06        | 95           |     |   |   |   |   |   |   |        |  |

|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docum<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |










| ID  | Task Name  | Duration          | Start              | Finish             | Predecessors | /06 |   |   |   |   |   |   | 3/6/06 |  |
|-----|--|-------------------|--------------------|--------------------|--------------|-----|---|---|---|---|---|---|--------|--|
|     |  |                   |                    |                    |              | T   | W | T | F | S | S | M | T      |  |
| 97  | Test Software/Hardware once installed                          | 2 days            | Fri 9/15/06        | Tue 9/19/06        | 96           |     |   |   |   |   |   |   |        |  |
| 98  | Train support staff  | 2 days            | Tue 9/19/06        | Thu 9/21/06        | 97           |     |   |   |   |   |   |   |        |  |
| 99  | Train Superusers   | 2 days            | Thu 9/21/06        | Mon 9/25/06        | 98           |     |   |   |   |   |   |   |        |  |
| 100 | Train Phase 1 Clinicians/HUC's                                 | 5 days            | Mon 9/25/06        | Mon 10/2/06        | 99           |     |   |   |   |   |   |   |        |  |
| 101 | Deploy software - Phase 1                                      | 15 days           | Mon 10/2/06        | Mon 10/23/06       | 100          |     |   |   |   |   |   |   |        |  |
| 102 | Train Phase 2 Clinicians/HUC's                                 | 6 days            | Tue 3/20/07        | Tue 3/27/07        |              |     |   |   |   |   |   |   |        |  |
| 103 | Deploy software - Phase 2                                      | 15 days           | Tue 3/20/07        | Mon 4/9/07         |              |     |   |   |   |   |   |   |        |  |
| 104 | Train Phase 3 Clinicians/HUC's                                 | 5 days            | Mon 6/11/07        | Fri 6/15/07        |              |     |   |   |   |   |   |   |        |  |
| 105 | Deploy software - Phase 3                                      | 15 days           | Wed 8/1/07         | Tue 8/21/07        |              |     |   |   |   |   |   |   |        |  |
| 106 | Deployment complete  | 0 days            | Thu 1/31/08        | Thu 1/31/08        | 105          |     |   |   |   |   |   |   |        |  |
| 107 | <b>Post Implementation Review/ Project Closure</b>             | <b>13.5 days?</b> | <b>Fri 2/1/08</b>  | <b>Wed 2/20/08</b> |              |     |   |   |   |   |   |   |        |  |
| 108 | CISES Tool   | 7 days            | Fri 2/1/08         | Mon 2/11/08        | 106          |     |   |   |   |   |   |   |        |  |
| 109 | Project deliverable approval                                   | 1 day?            | Tue 2/12/08        | Tue 2/12/08        | 108          |     |   |   |   |   |   |   |        |  |
| 110 | Post-Implementation Project Risk Management Plan               | 3 days            | Wed 2/13/08        | Fri 2/15/08        | 109          |     |   |   |   |   |   |   |        |  |
| 111 | <b>Vendor Contract Closure Procedure</b>                       | <b>1 day?</b>     | <b>Mon 2/18/08</b> | <b>Mon 2/18/08</b> | <b>110</b>   |     |   |   |   |   |   |   |        |  |
| 112 | Recommended Corrective Actions                                 | 1 day?            | Mon 2/18/08        | Mon 2/18/08        |              |     |   |   |   |   |   |   |        |  |
| 113 | Contract Documentation/Closure                                 | 1 day?            | Mon 2/18/08        | Mon 2/18/08        |              |     |   |   |   |   |   |   |        |  |
| 114 | Procurement management plan update                             | 1 day?            | Mon 2/18/08        | Mon 2/18/08        |              |     |   |   |   |   |   |   |        |  |
| 115 | Contract management plan update/handoff                        | 1 day?            | Mon 2/18/08        | Mon 2/18/08        |              |     |   |   |   |   |   |   |        |  |
| 116 | <b>Document lessons learned</b>                                | <b>2.5 days?</b>  | <b>Mon 2/18/08</b> | <b>Wed 2/20/08</b> |              |     |   |   |   |   |   |   |        |  |
| 117 | <a href="#">Archive project documents</a>                      | 1 day?            | Mon 2/18/08        | Mon 2/18/08        |              |     |   |   |   |   |   |   |        |  |
| 118 | Distribute to team members                                     | 0.5 days          | Tue 2/19/08        | Tue 2/19/08        | 117          |     |   |   |   |   |   |   |        |  |
| 119 | Create software maintenance team                               | 1 day             | Tue 2/19/08        | Wed 2/20/08        | 118          |     |   |   |   |   |   |   |        |  |
| 120 | Release Unneeded Resources back to their departments           | 0 days            | Wed 2/20/08        | Wed 2/20/08        | 119          |     |   |   |   |   |   |   |        |  |
| 121 | Post implementation review complete                            | 0 days            | Wed 2/20/08        | Wed 2/20/08        | 120          |     |   |   |   |   |   |   |        |  |
| 122 | Nursing & Patient Documentation System Implementation Complete | 0 days            | Wed 2/20/08        | Wed 2/20/08        | 121          |     |   |   |   |   |   |   |        |  |

|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |














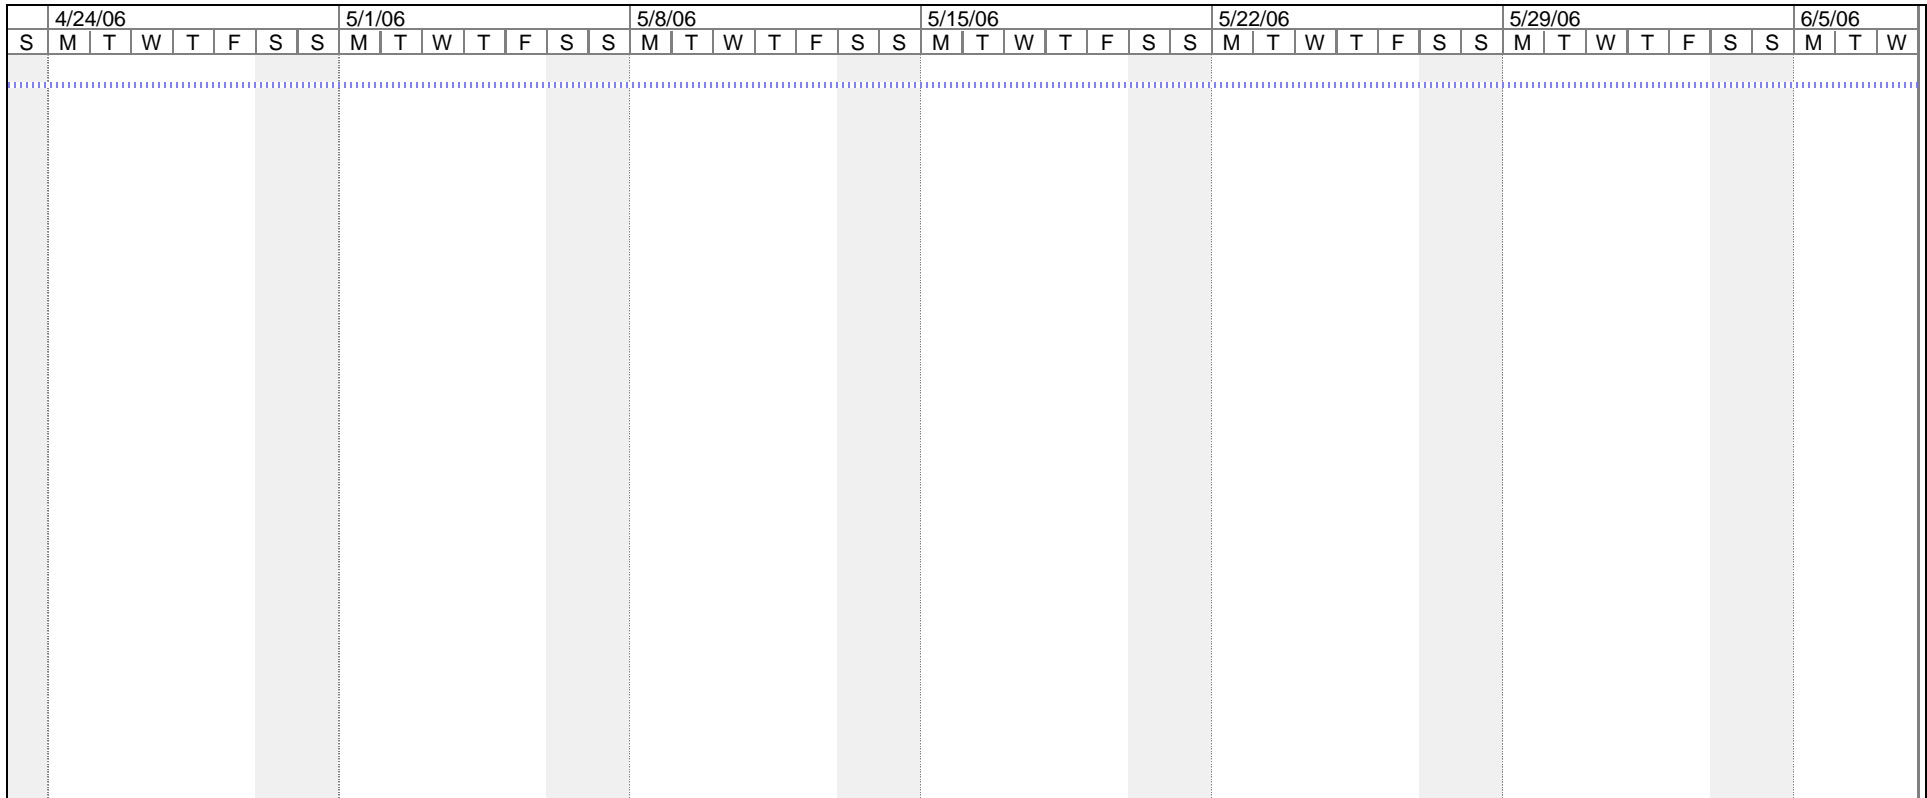
|   |   |   |   |   | 3/13/06 |   |   |   |   | 3/20/06 |   |   |   |   | 3/27/06 |   |   |   |   | 4/3/06 |   |   |   |   | 4/10/06 |   |   |   |   | 4/17/06 |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
|---|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|--------|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| W | T | F | S | S | M       | T | W | T | F | S       | S | M | T | W | T       | F | S | S | M | T      | W | T | F | S | S       | M | T | W | T | F       | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S | S |
|   |   |   |   |   |         |   |   |   |   |         |   |   |   |   |         |   |   |   |   |        |   |   |   |   |         |   |   |   |   |         |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |

|  |  |   |  |
|--|--|---|--|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task      | Milestone        | External Tasks      |
|  | Split     | Summary          | External Milestone  |
|  | Progress  | Project Summary  | Deadline            |


|   |   |   |   |   | 3/13/06 |   |   |   |   | 3/20/06 |   |   |   |   | 3/27/06 |   |   |   |   | 4/3/06 |   |   |   |   | 4/10/06 |   |   |   |   | 4/17/06 |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |
|---|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|--------|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|--|--|--|--|--|--|--|--|
| W | T | F | S | S | M       | T | W | T | F | S       | S | M | T | W | T       | F | S | S | M | T      | W | T | F | S | S       | M | T | W | T | F       | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S |  |  |  |  |  |  |  |  |
|   |   |   |   |   |         |   |   |   |   |         |   |   |   |   |         |   |   |   |   |        |   |   |   |   |         |   |   |   |   |         |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |



|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |




I,Interface Developer

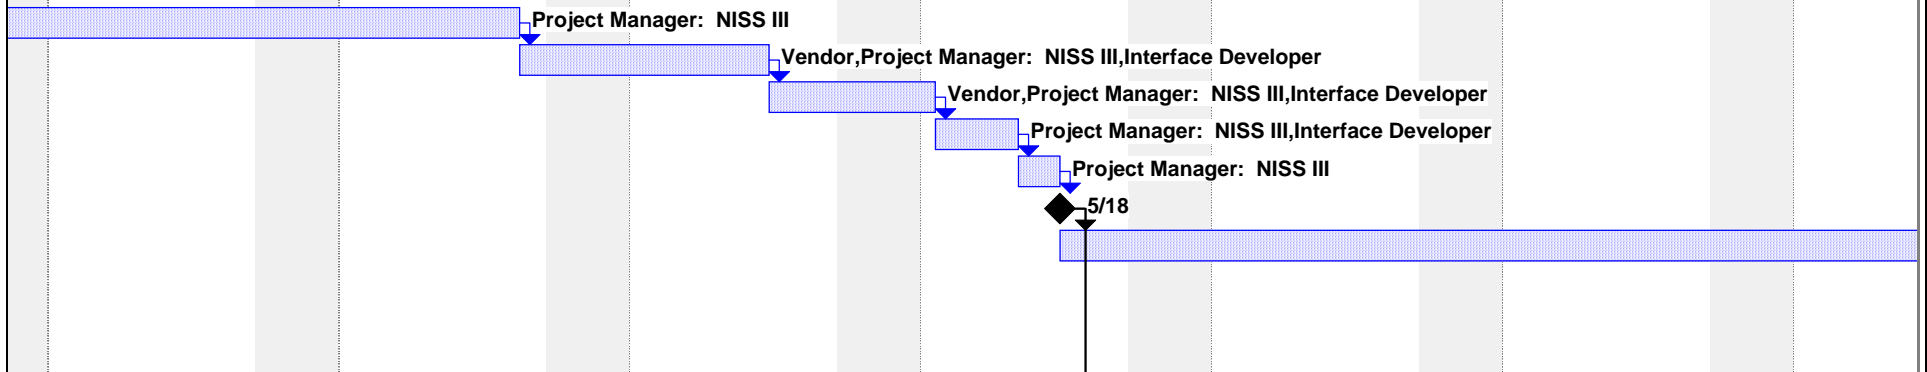

Project: Nursing & Patient Care Docun  
Date: Mon 4/10/06

|          |  |                 |  |                    |  |
|----------|--|-----------------|--|--------------------|--|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |

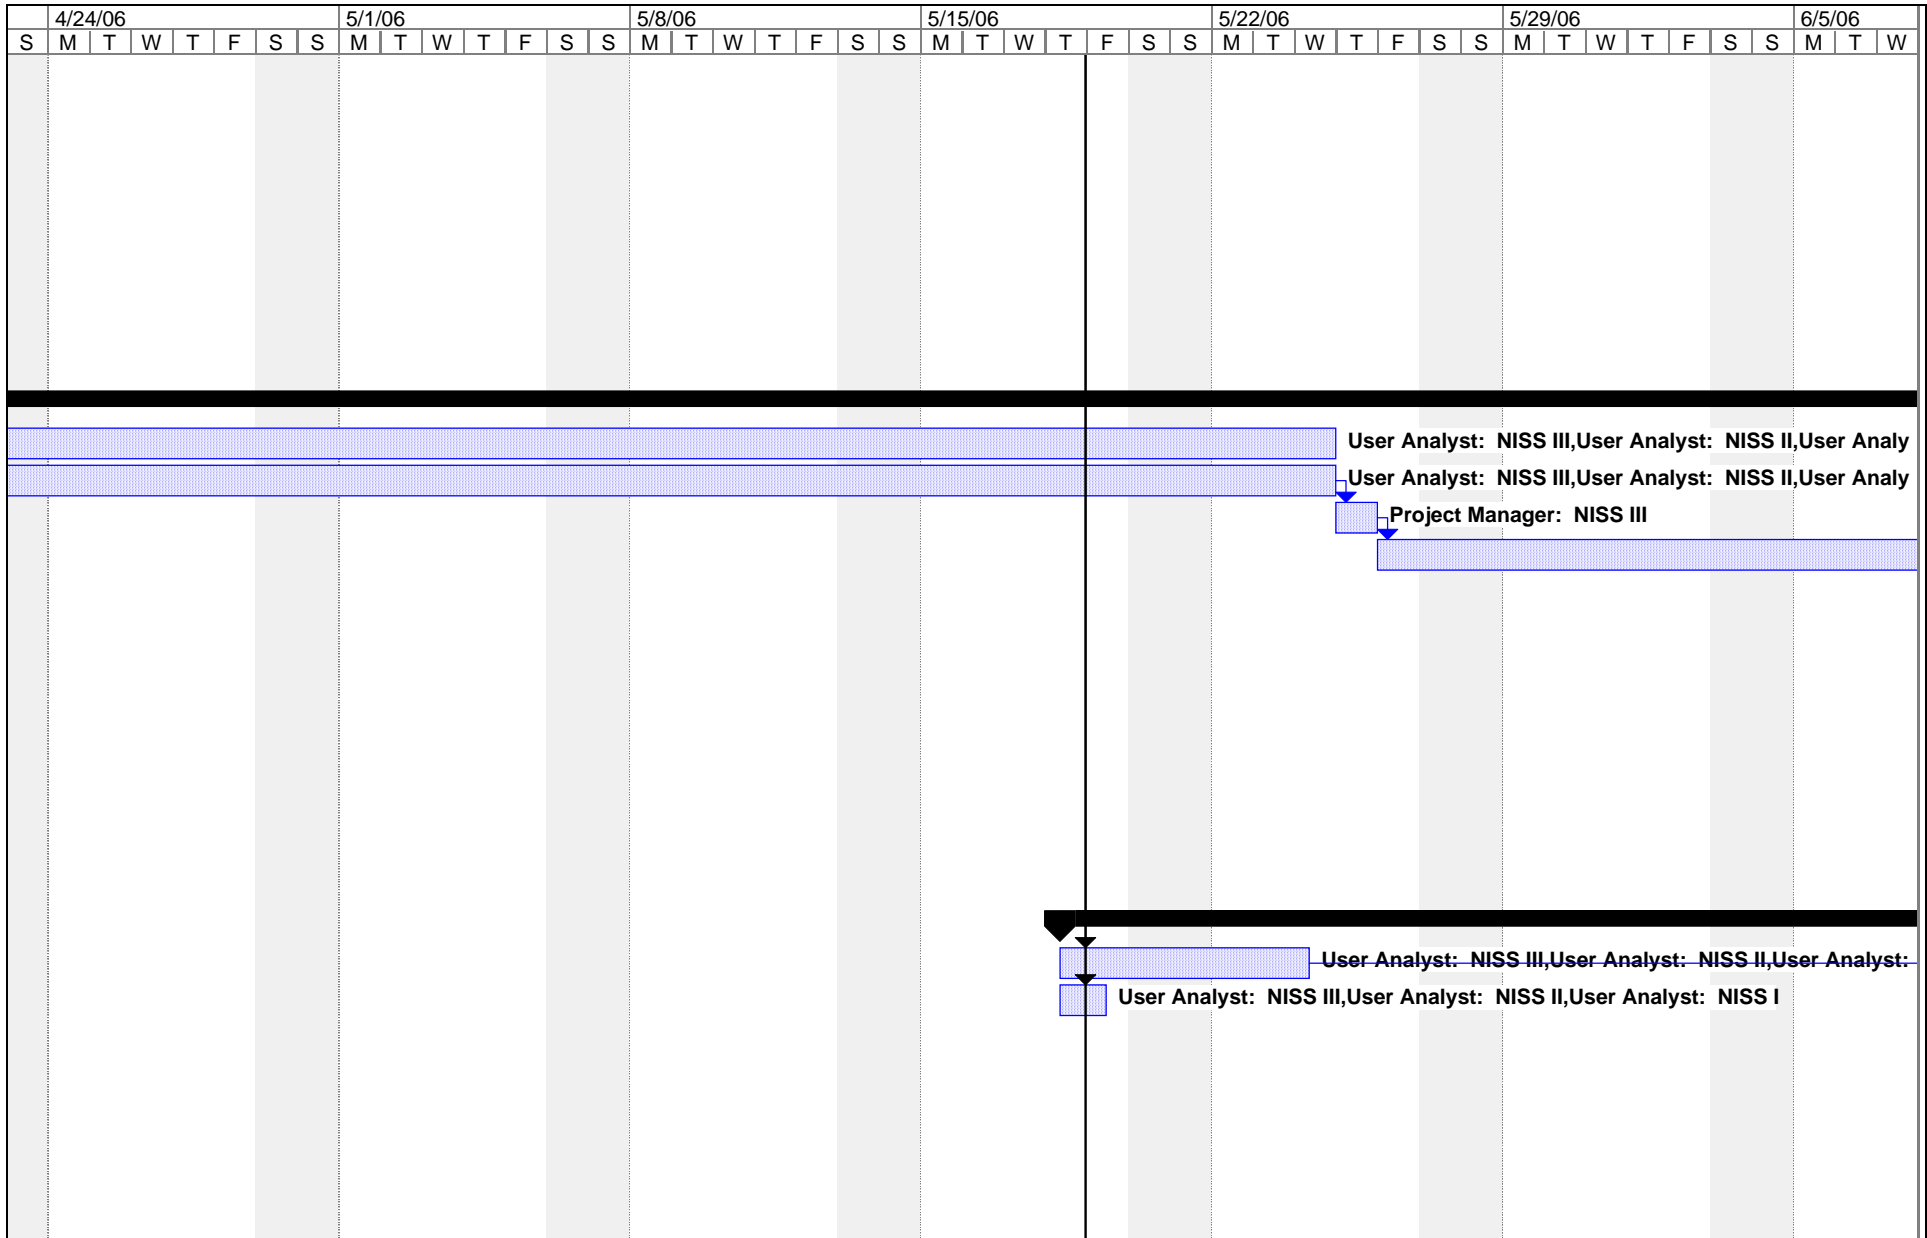










Project: Nursing & Patient Care Docun  
 Date: Mon 4/10/06


|          |  |                 |  |                    |  |
|----------|--|-----------------|--|--------------------|--|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |




| 4/24/06 |   |   |   |   |   |   | 5/1/06 |   |   |   |   |   |   | 5/8/06 |   |   |   |   |   |   | 5/15/06 |   |   |   |   |   |   | 5/22/06 |   |   |   |   |   |   | 5/29/06 |   |   |   |   |   |   | 6/5/06 |   |   |   |  |
|---------|---|---|---|---|---|---|--------|---|---|---|---|---|---|--------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|--------|---|---|---|--|
| S       | M | T | W | T | F | S | S      | M | T | W | T | F | S | S      | M | T | W | T | F | S | S       | M | T | W | T | F | S | S       | M | T | W | T | F | S | S       | M | T | W | T | F | S | S      | M | T | W |  |
|         |   |   |   |   |   |   |        |   |   |   |   |   |   |        |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |   |   |   |        |   |   |   |  |

|  |
|--|
|  |
|--|

|  |  |   |  |
|--|--|---|--|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task      | Milestone        | External Tasks      |
|  | Split     | Summary          | External Milestone  |
|  | Progress  | Project Summary  | Deadline            |

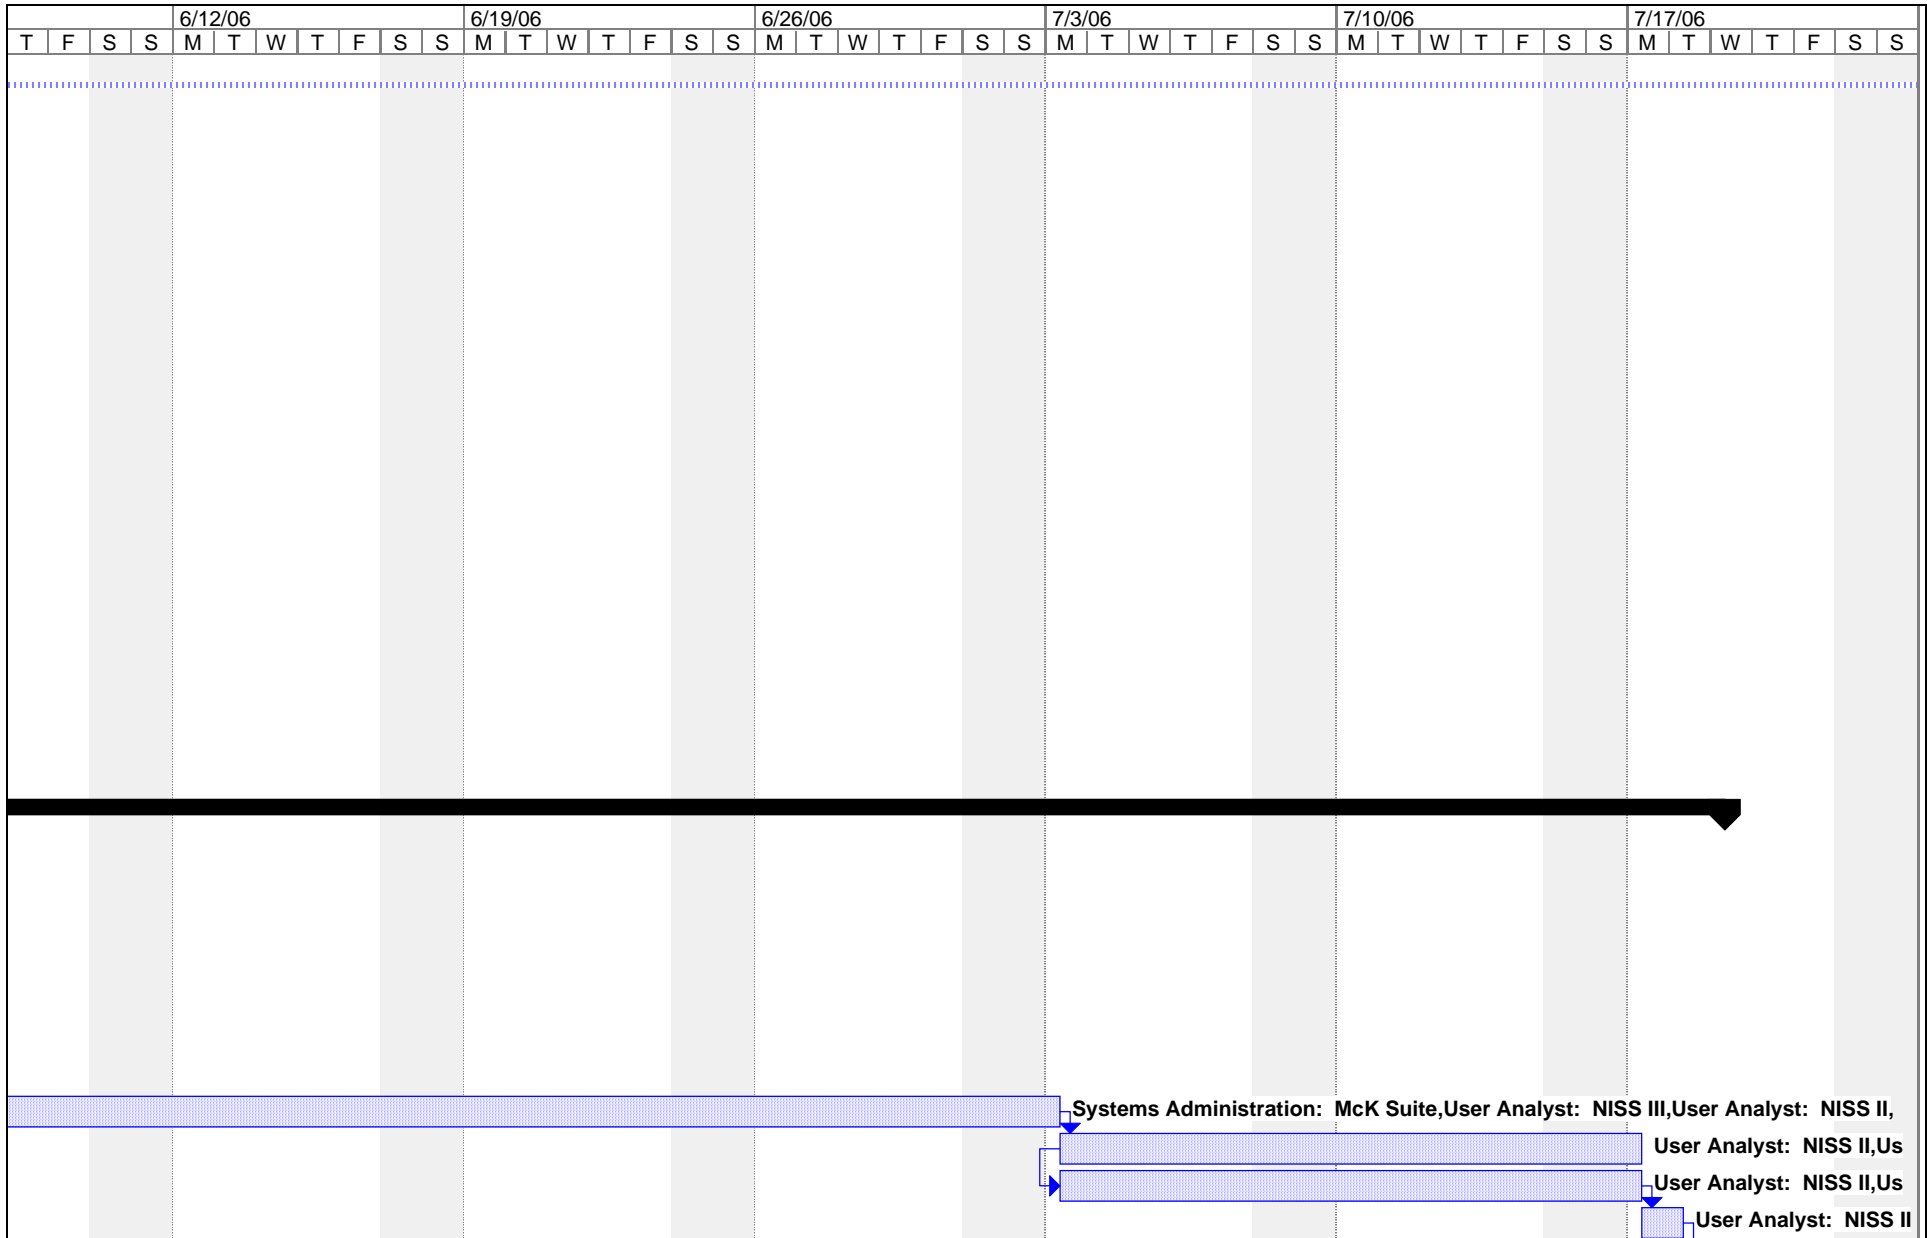



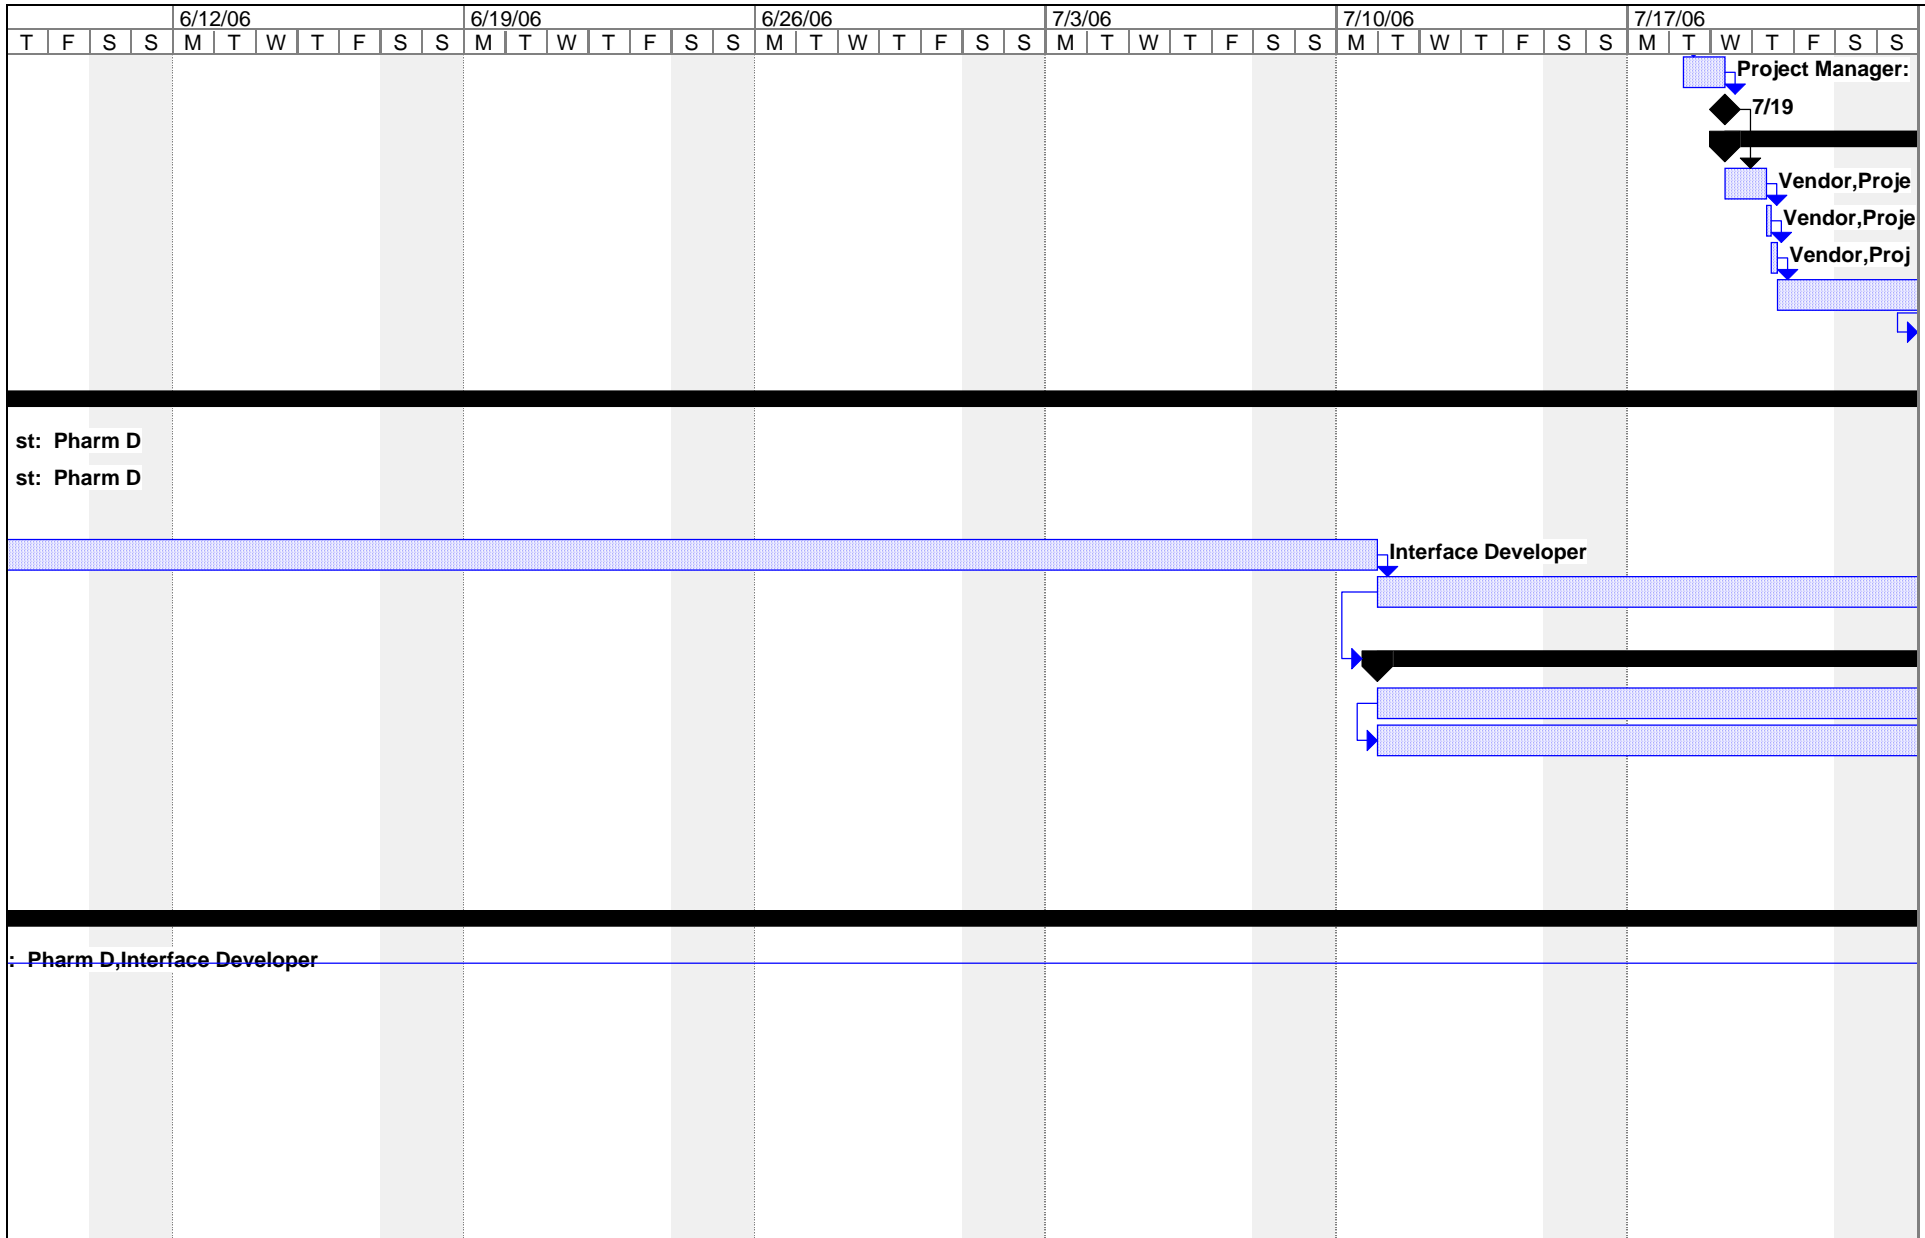






|  |          |  |                 |  |                    |  |
|--|----------|--|-----------------|--|--------------------|--|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |



Project: Nursing & Patient Care Docun  
Date: Mon 4/10/06










|          |  |                 |  |                    |  |
|----------|--|-----------------|--|--------------------|--|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |

|   |   |   |   | 6/12/06 |   |   |   | 6/19/06 |   |   |   | 6/26/06 |   |   |   | 7/3/06 |   |   |   | 7/10/06 |   |   |   | 7/17/06 |   |   |   |   |   |   |   |  |  |  |  |
|---|---|---|---|---------|---|---|---|---------|---|---|---|---------|---|---|---|--------|---|---|---|---------|---|---|---|---------|---|---|---|---|---|---|---|--|--|--|--|
| T   | F | S | S | M       | T | W | T | F       | S | S | M | T       | W | T | F | S      | S | M | T | W       | T | F | S | S       | M | T | W | T | F | S | S |  |  |  |  |
|   |   |   |   |         |   |   |   |         |   |   |   |         |   |   |   |        |   |   |   |         |   |   |   |         |   |   |   |   |   |   |   |  |  |  |  |
| <b>r,Help Desk 1</b>  |   |   |   |         |   |   |   |         |   |   |   |         |   |   |   |        |   |   |   |         |   |   |   |         |   |   |   |   |   |   |   |  |  |  |  |
| <b>r,Help Desk 1</b>  |   |   |   |         |   |   |   |         |   |   |   |         |   |   |   |        |   |   |   |         |   |   |   |         |   |   |   |   |   |   |   |  |  |  |  |
| <b>lp-Desk 1</b>  |   |   |   |         |   |   |   |         |   |   |   |         |   |   |   |        |   |   |   |         |   |   |   |         |   |   |   |   |   |   |   |  |  |  |  |
| <b>,Desktop Support 2</b>   |   |   |   |         |   |   |   |         |   |   |   |         |   |   |   |        |   |   |   |         |   |   |   |         |   |   |   |   |   |   |   |  |  |  |  |
| <b>te,Systems Administration: Mck Suite,Interface Developer,Outcomes/Reports Analyst: NISS II</b> |   |   |   |         |   |   |   |         |   |   |   |         |   |   |   |        |   |   |   |         |   |   |   |         |   |   |   |   |   |   |   |  |  |  |  |










|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |


|   |   |   |   | 6/12/06 |   |   |   | 6/19/06 |   |   |   | 6/26/06 |   |   |   | 7/3/06 |   |   |   | 7/10/06 |   |   |   | 7/17/06 |   |   |   |   |   |   |   |  |  |  |  |
|---|---|---|---|---------|---|---|---|---------|---|---|---|---------|---|---|---|--------|---|---|---|---------|---|---|---|---------|---|---|---|---|---|---|---|--|--|--|--|
| T | F | S | S | M       | T | W | T | F       | S | S | M | T       | W | T | F | S      | S | M | T | W       | T | F | S | S       | M | T | W | T | F | S | S |  |  |  |  |
|   |   |   |   |         |   |   |   |         |   |   |   |         |   |   |   |        |   |   |   |         |   |   |   |         |   |   |   |   |   |   |   |  |  |  |  |

|  |
|--|
|  |
|--|


|  |  |   |  |
|--|--|---|--|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task      | Milestone        | External Tasks      |
|  | Split     | Summary          | External Milestone  |
|  | Progress  | Project Summary  | Deadline            |

| 7/24/06  |   |   |   |   |   |   | 7/31/06 |   |   |   |   |   |   | 8/7/06 |   |   |   |   |   |   | 8/14/06 |   |   |   |   |   |   | 8/21/06 |   |   |   |   |   |   | 8/28/06 |   |   |   |   |   |   | 9/4/06 |   |   |   |  |  |  |
|--|---|---|---|---|---|---|---------|---|---|---|---|---|---|--------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|--------|---|---|---|--|--|--|
| M  | T | W | T | F | S | S | M       | T | W | T | F | S | S | M      | T | W | T | F | S | S | M       | T | W | T | F | S | S | M       | T | W | T | F | S | S | M       | T | W | T | F | S | S | M      | T | W | T |  |  |  |
| <p>Network Administration: Mck Suite<br/>           er Analyst: NISS I<br/>           er Analyst: NISS I<br/>           I,User Analyst: NISS I</p> |   |   |   |   |   |   |         |   |   |   |   |   |   |        |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |   |   |   |        |   |   |   |  |  |  |

|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |

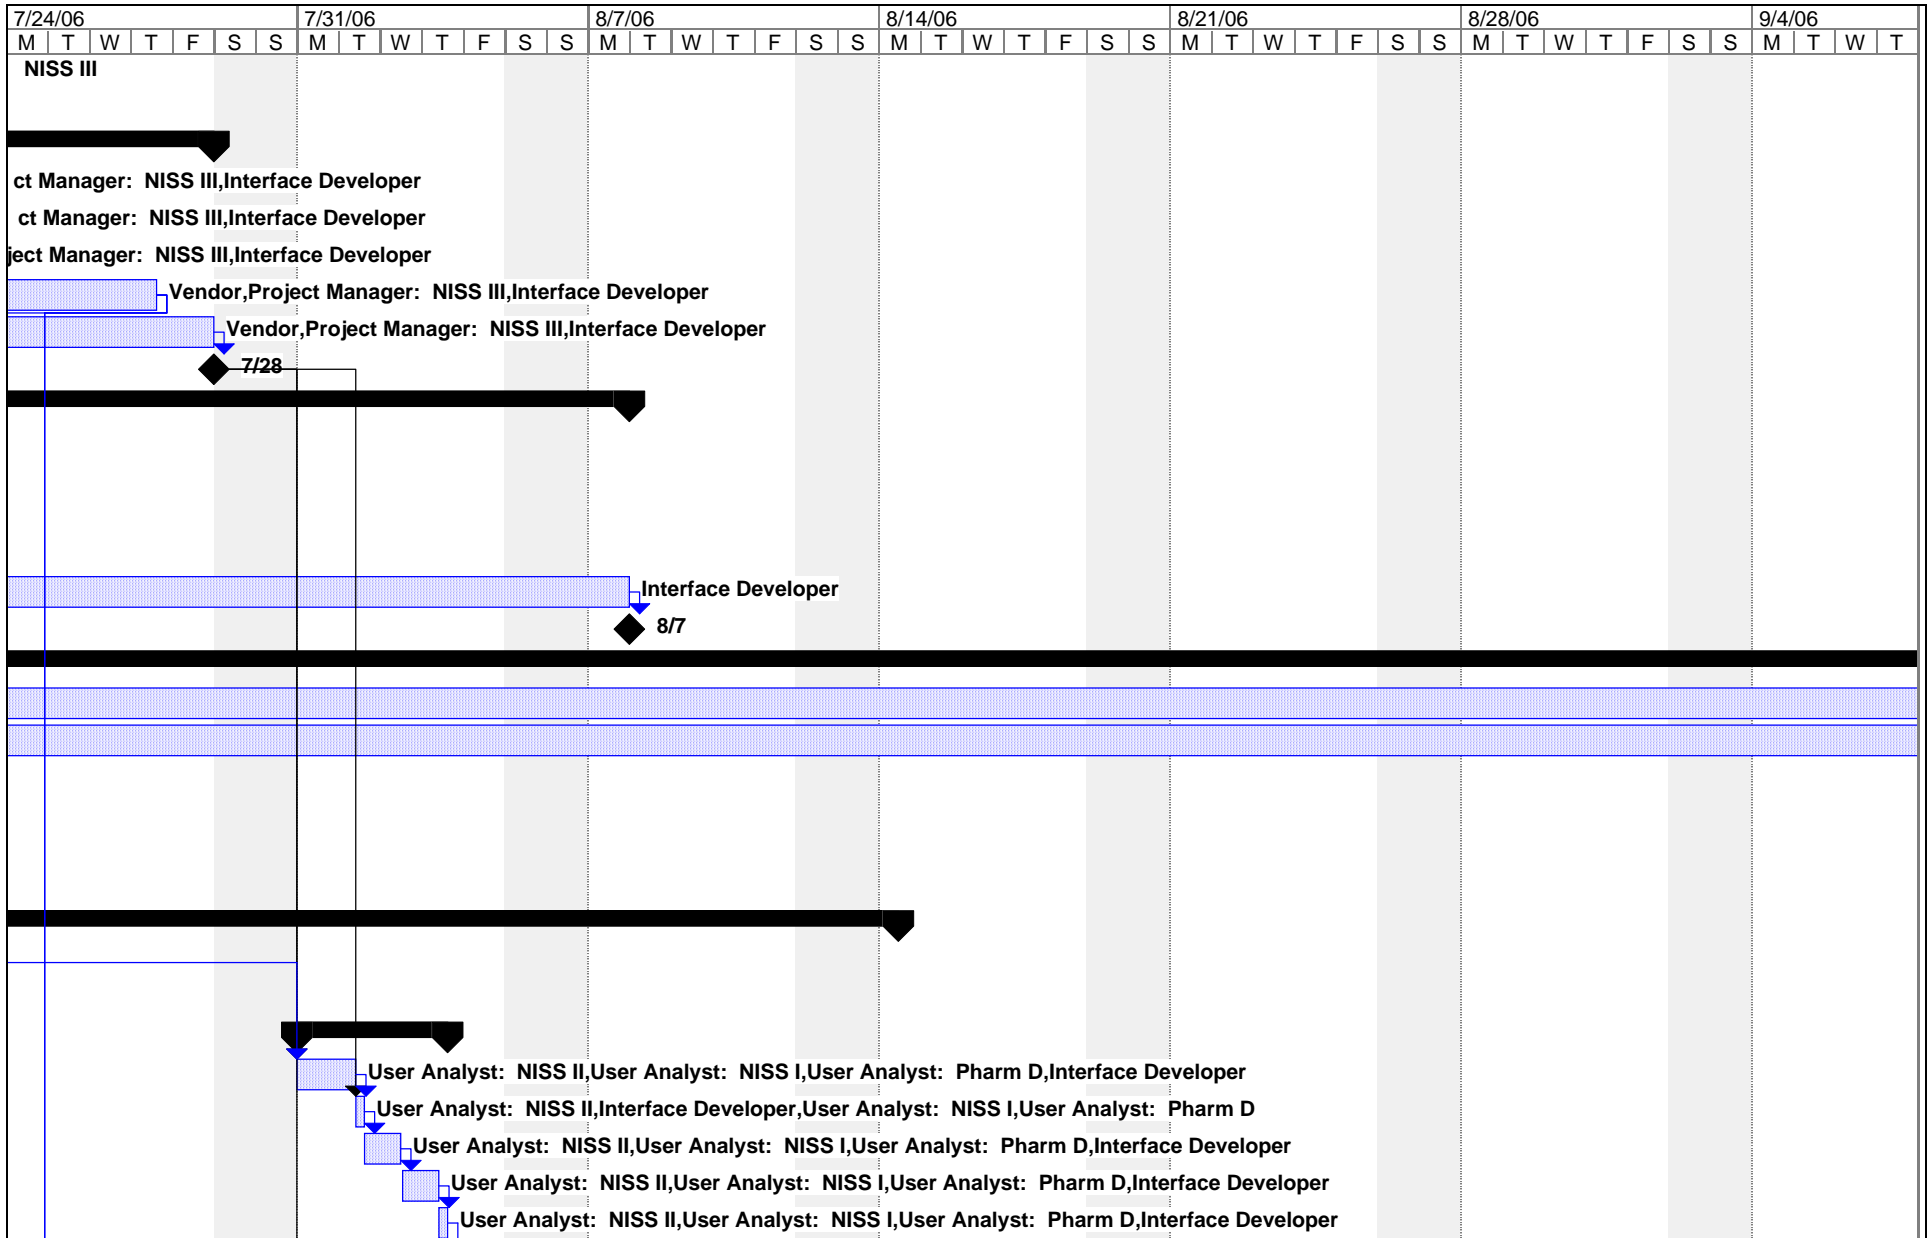



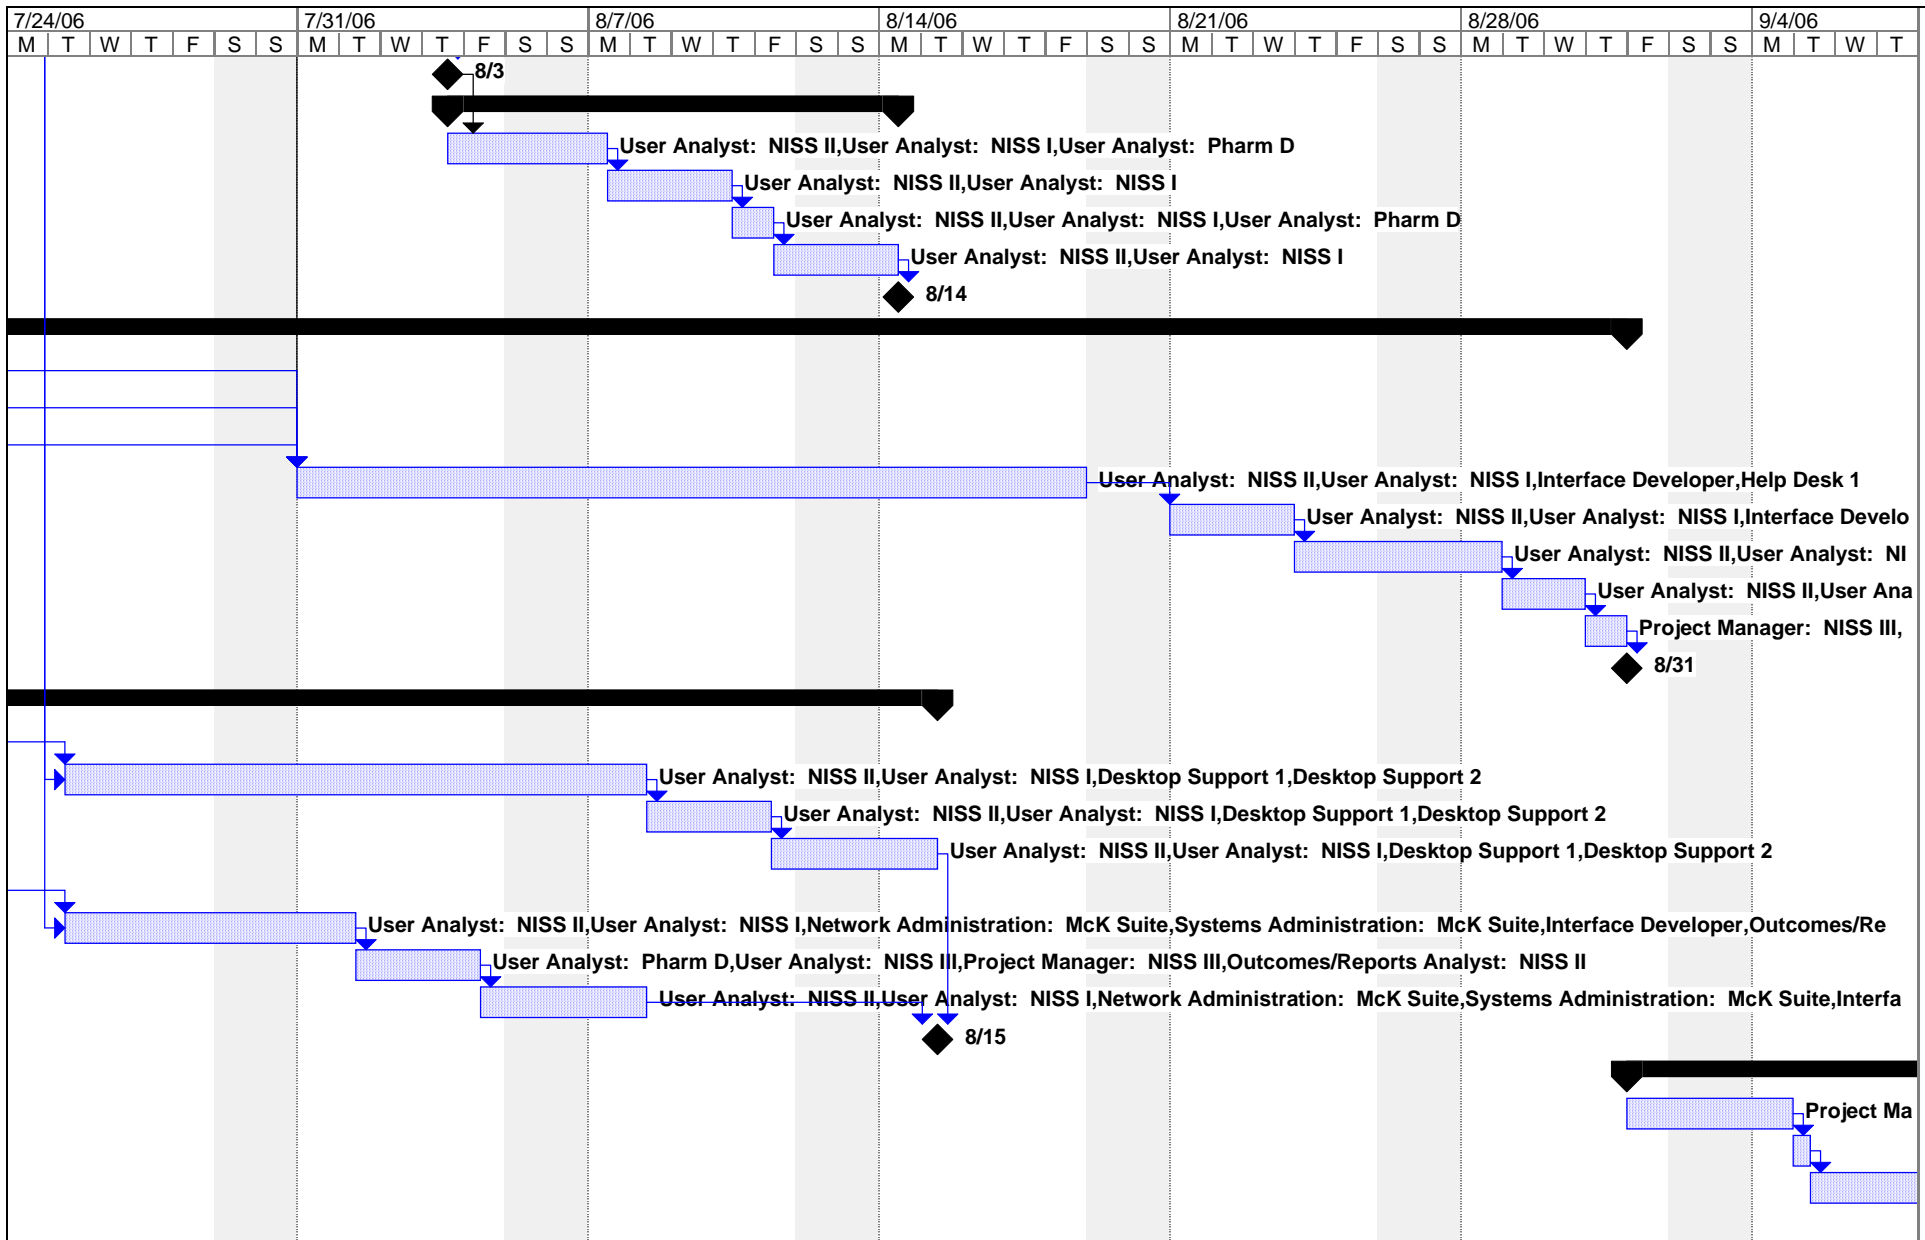






|  |          |  |                 |  |                    |  |
|--|----------|--|-----------------|--|--------------------|--|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |












|  |          |  |                 |  |                    |  |
|--|----------|--|-----------------|--|--------------------|--|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |


| 7/24/06 |   |   |   |   |   |   | 7/31/06 |   |   |   |   |   |   | 8/7/06 |   |   |   |   |   |   | 8/14/06 |   |   |   |   |   |   | 8/21/06 |   |   |   |   |   |   | 8/28/06 |   |   |   |   |   |   | 9/4/06 |   |   |   |  |  |  |
|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|--------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|--------|---|---|---|--|--|--|
| M       | T | W | T | F | S | S | M       | T | W | T | F | S | S | M      | T | W | T | F | S | S | M       | T | W | T | F | S | S | M       | T | W | T | F | S | S | M       | T | W | T | F | S | S | M      | T | W | T |  |  |  |
|         |   |   |   |   |   |   |         |   |   |   |   |   |   |        |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |   |   |   |        |   |   |   |  |  |  |



|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |

| 9/11/06                |   |   | 9/18/06 |   |   | 9/25/06 |   |   | 10/2/06 |   |   | 10/9/06 |   |   | 10/16/06 |   |   | 10/23/06 |   |   |   |   |   |   |   |   |   |   |   |   |   |
|------------------------|---|---|---------|---|---|---------|---|---|---------|---|---|---------|---|---|----------|---|---|----------|---|---|---|---|---|---|---|---|---|---|---|---|---|
| F                      | S | S | M       | T | W | T       | F | S | S       | M | T | W       | T | F | S        | S | M | T        | W | T | F | S | S | M | T | W | T | F | S | S | M |
| Empty Gantt chart area |   |   |         |   |   |         |   |   |         |   |   |         |   |   |          |   |   |          |   |   |   |   |   |   |   |   |   |   |   |   |   |

|  |  |   |  |
|--|--|---|--|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task      | Milestone        | External Tasks      |
|  | Split     | Summary          | External Milestone  |
|  | Progress  | Project Summary  | Deadline            |

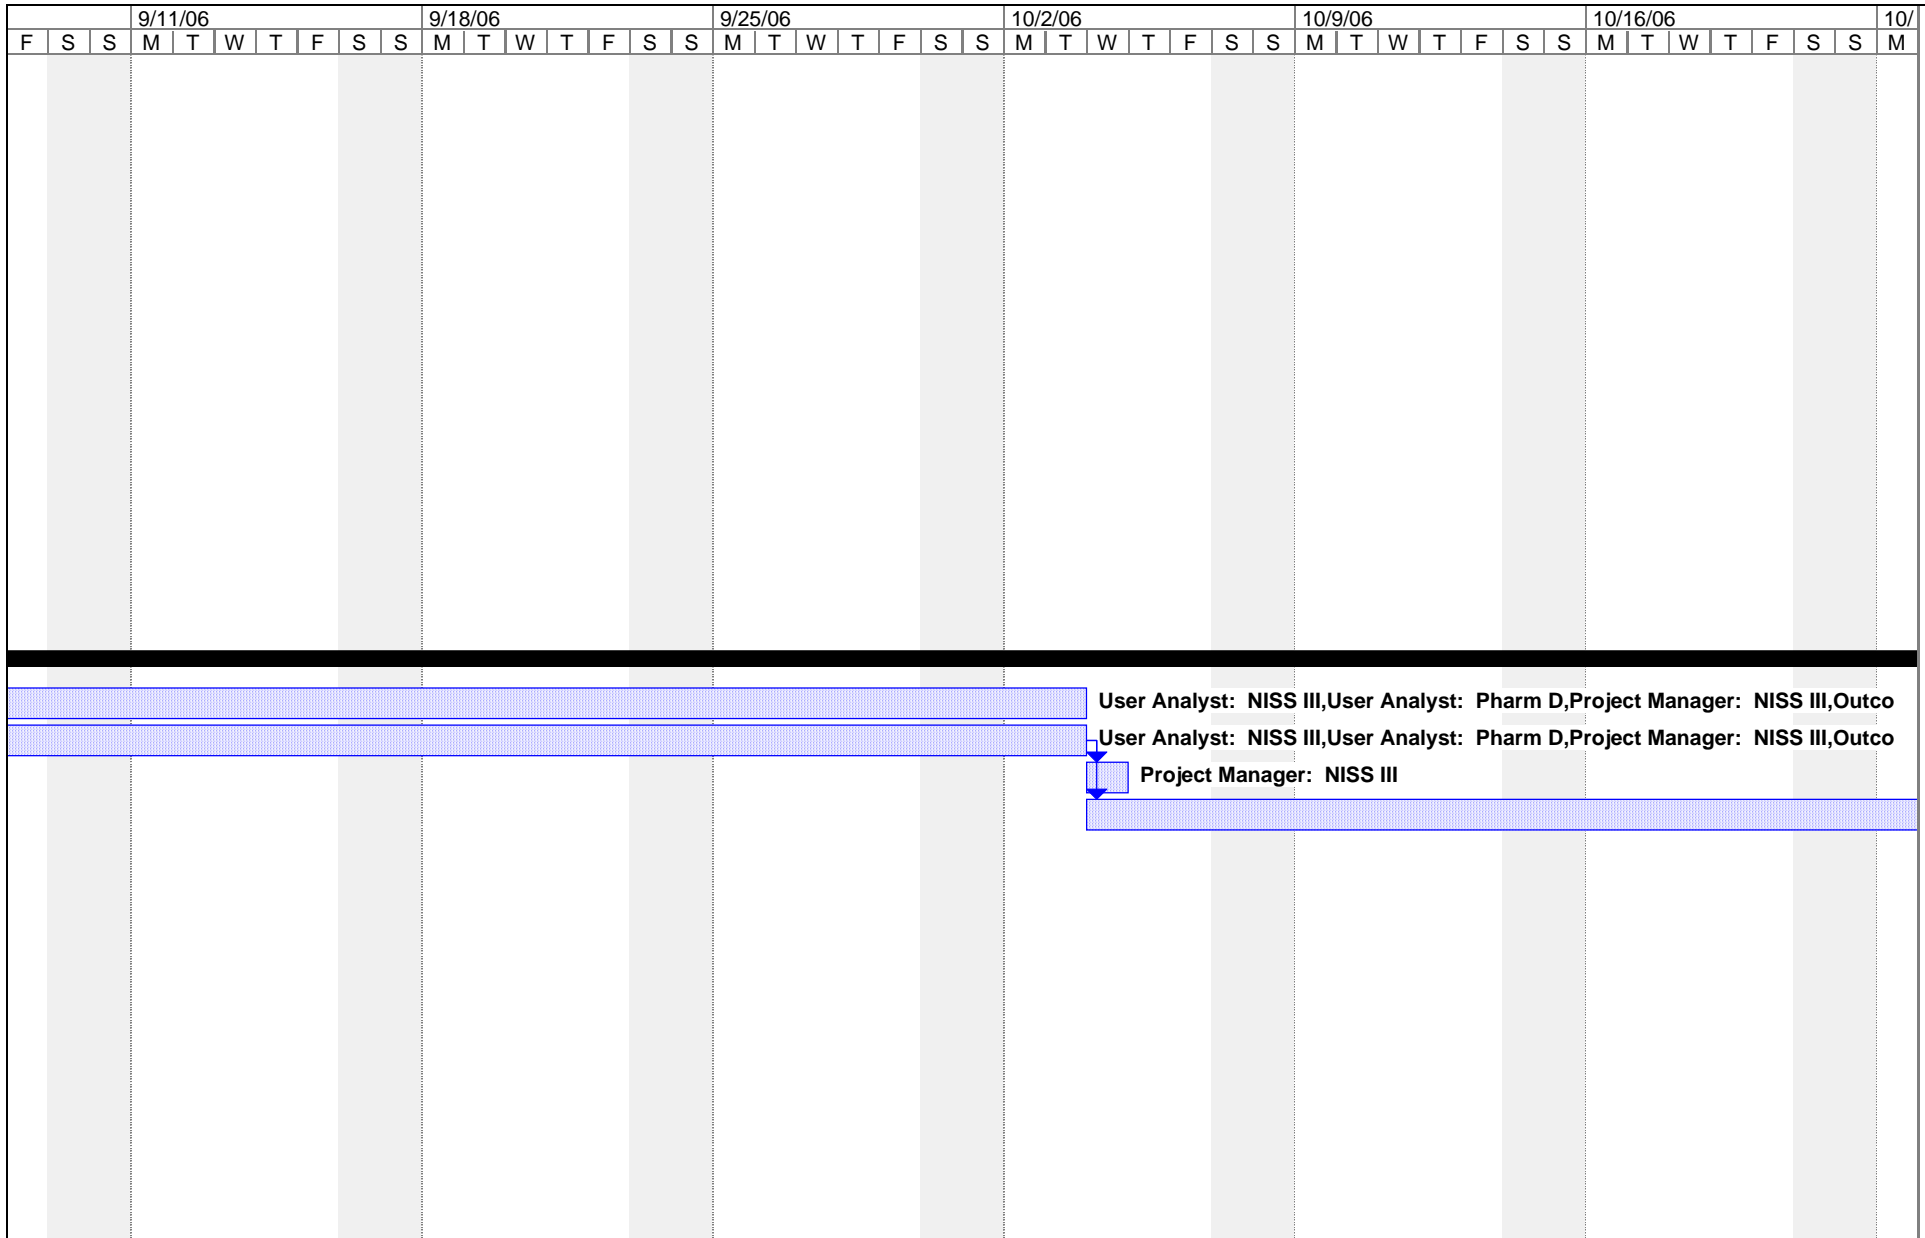


User Analyst: NISS III, User Analyst: Pharm D, Project Manager: NISS III, Outco  
 User Analyst: NISS III, User Analyst: Pharm D, Project Manager: NISS III, Outco  
 Project Manager: NISS III


Project: Nursing & Patient Care Docun  
 Date: Mon 4/10/06



|  |          |  |                 |  |                    |  |
|--|----------|--|-----------------|--|--------------------|--|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |

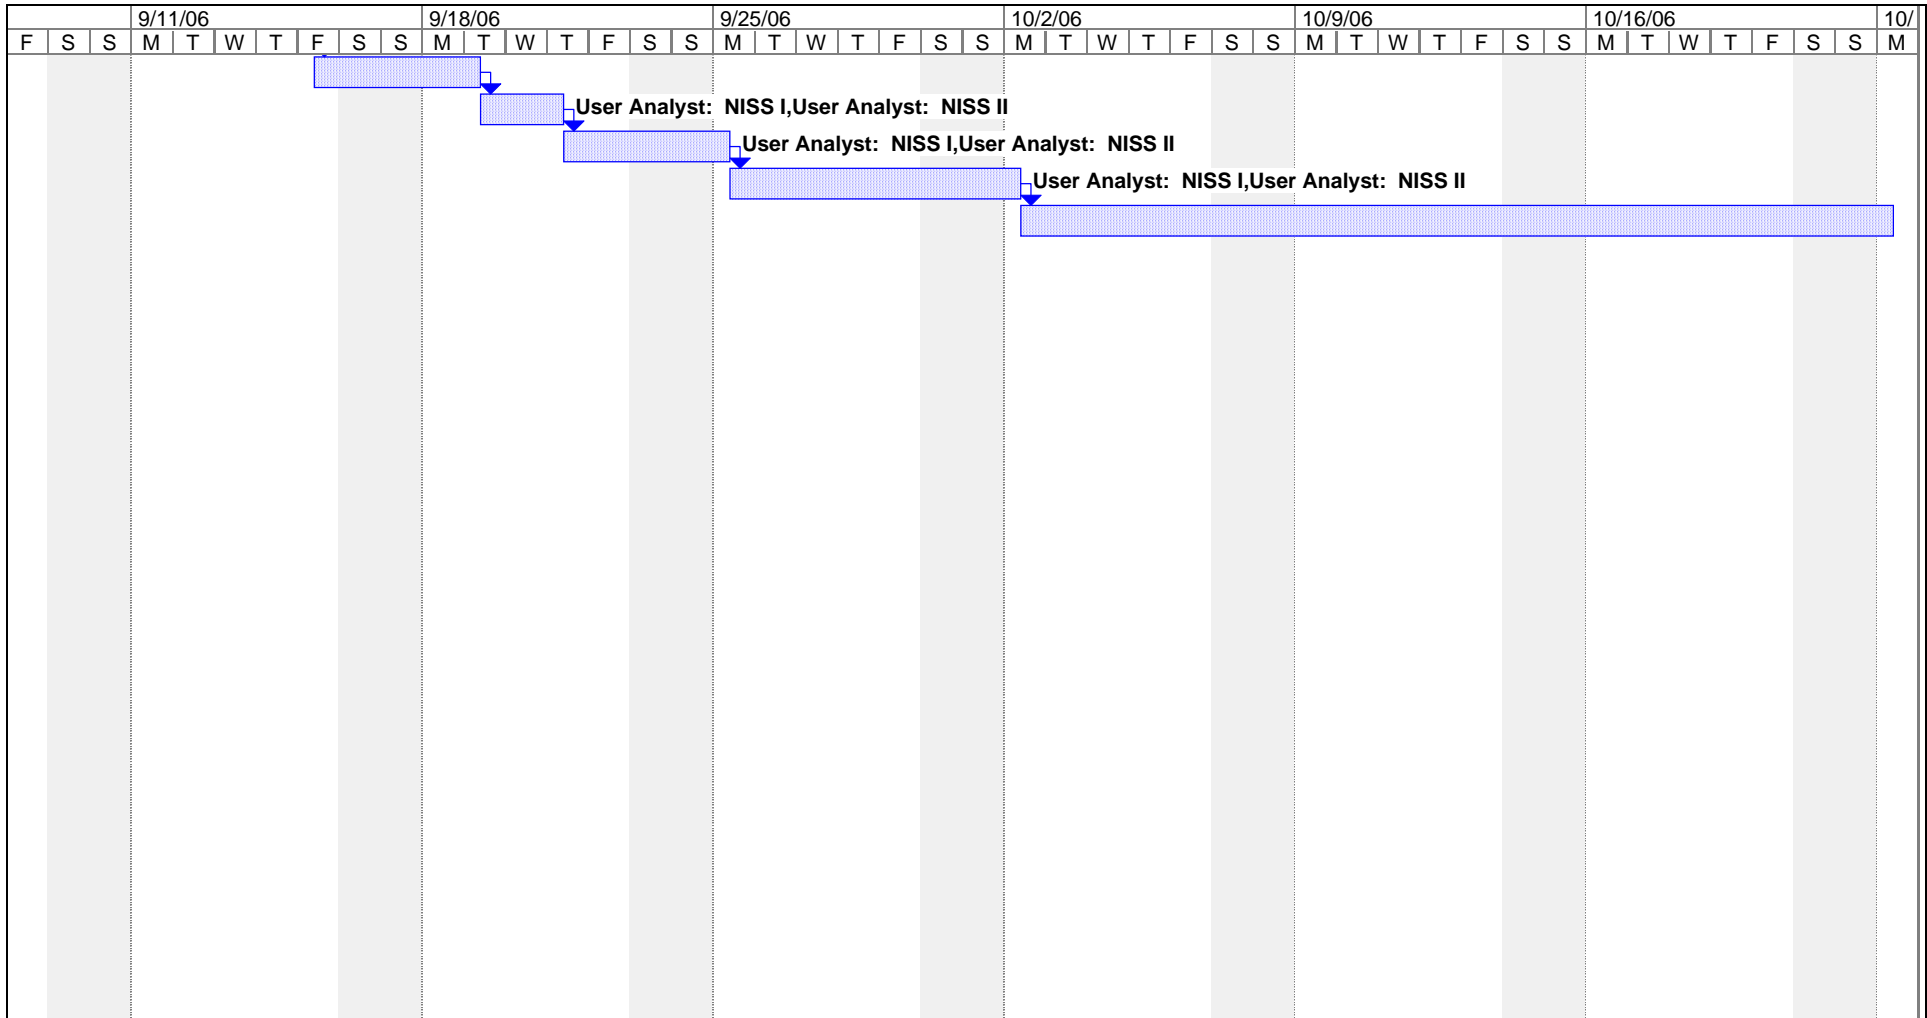


Project: Nursing & Patient Care Docun  
 Date: Mon 4/10/06







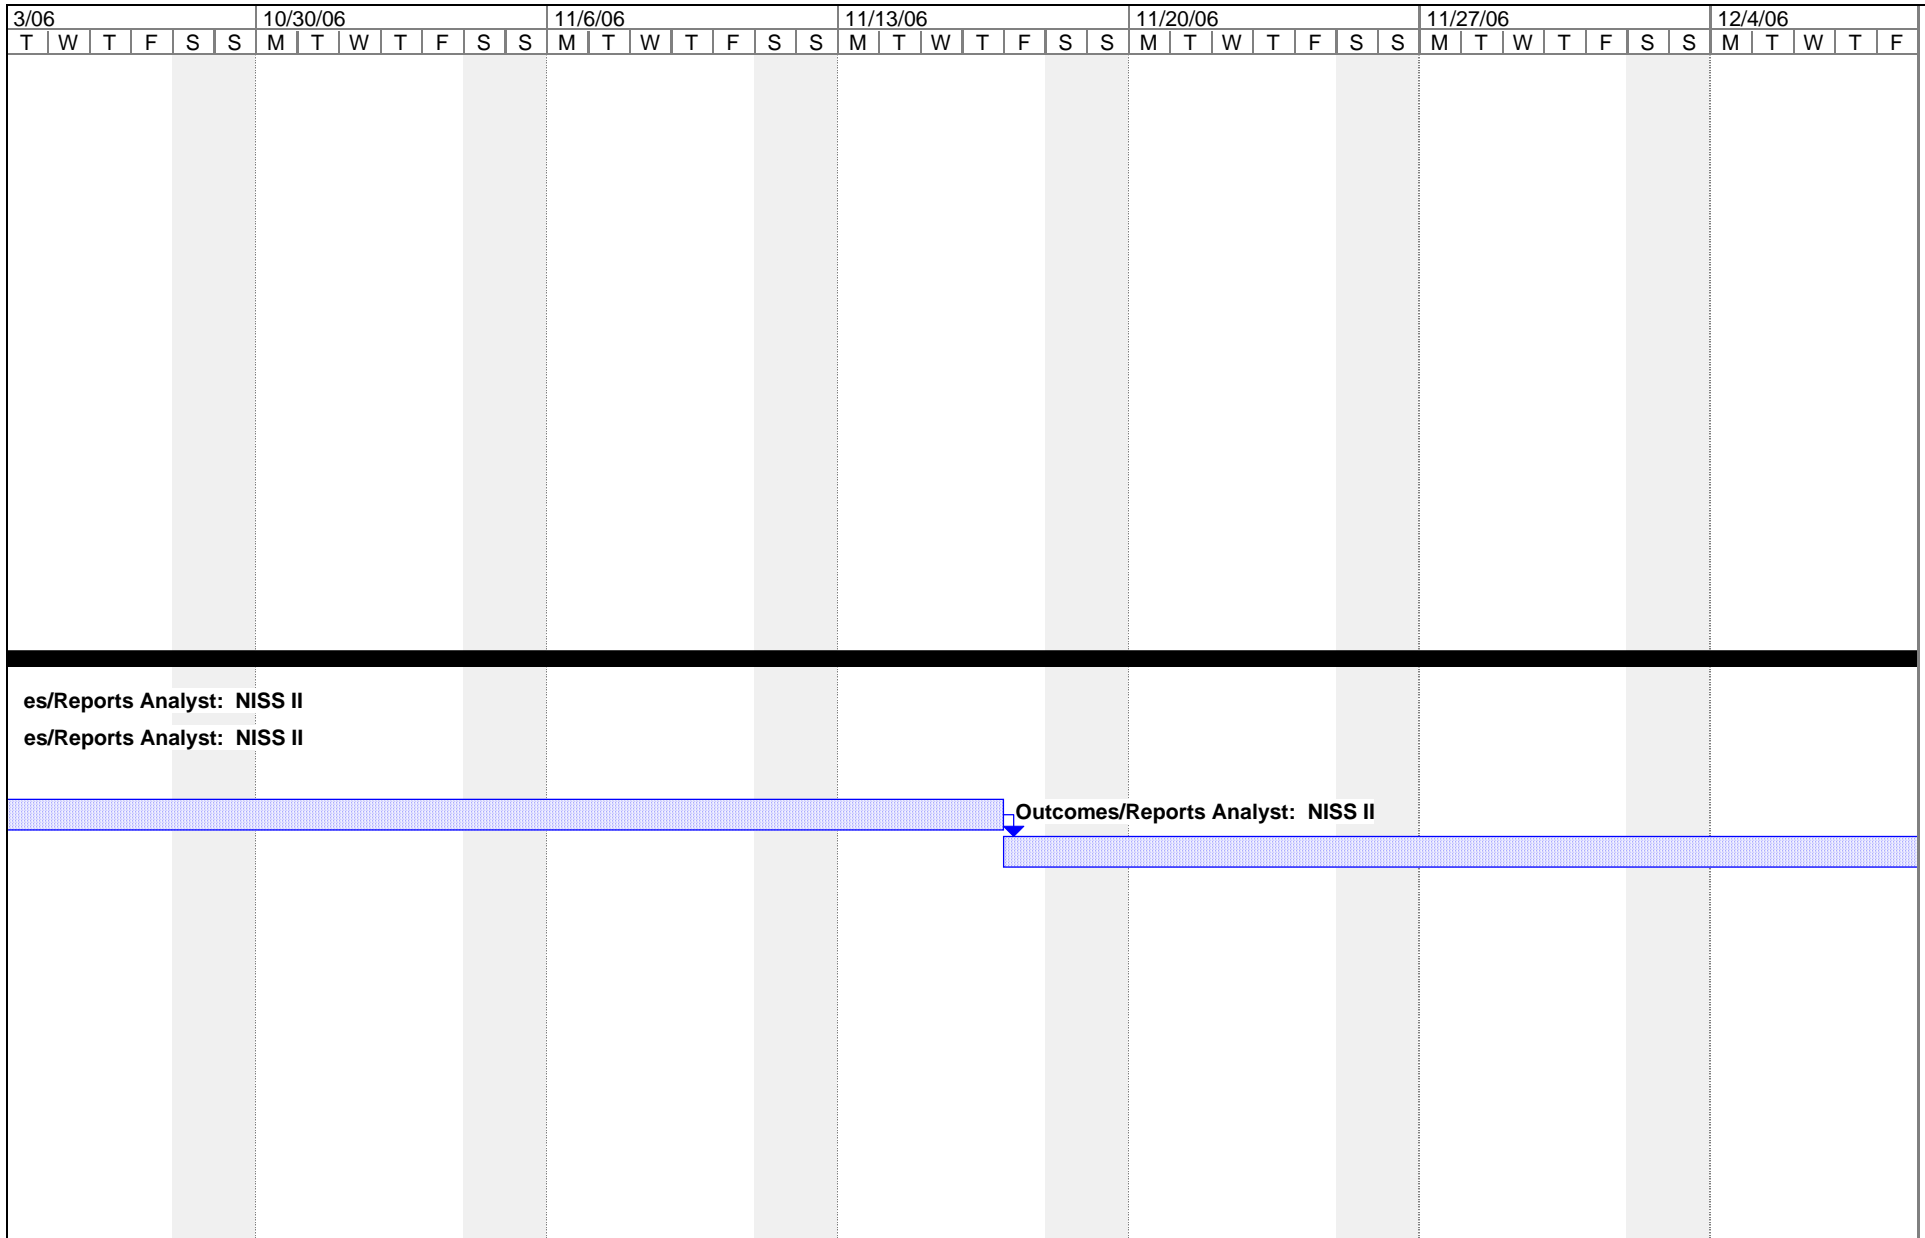


|          |   |                 |   |                    |   |
|----------|---|-----------------|---|--------------------|---|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |












Project: Nursing & Patient Care Docun  
Date: Mon 4/10/06

|          |   |                 |   |                    |   |
|----------|---|-----------------|---|--------------------|---|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |












|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |

| 3/06 |   |   |   |   |   | 10/30/06 |   |   |   |   |   | 11/6/06 |   |   |   |   |   | 11/13/06 |   |   |   |   |   | 11/20/06 |   |   |   |   |   | 11/27/06 |   |   |   |   |   | 12/4/06 |   |   |   |   |   |   |   |   |   |
|------|---|---|---|---|---|----------|---|---|---|---|---|---------|---|---|---|---|---|----------|---|---|---|---|---|----------|---|---|---|---|---|----------|---|---|---|---|---|---------|---|---|---|---|---|---|---|---|---|
| T    | W | T | F | S | S | M        | T | W | T | F | S | S       | M | T | W | T | F | S        | S | M | T | W | T | F        | S | S | M | T | W | T        | F | S | S | M | T | W       | T | F | S | S | M | T | W | T | F |
|      |   |   |   |   |   |          |   |   |   |   |   |         |   |   |   |   |   |          |   |   |   |   |   |          |   |   |   |   |   |          |   |   |   |   |   |         |   |   |   |   |   |   |   |   |   |
|      |   |   |   |   |   |          |   |   |   |   |   |         |   |   |   |   |   |          |   |   |   |   |   |          |   |   |   |   |   |          |   |   |   |   |   |         |   |   |   |   |   |   |   |   |   |

|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |


| 3/06   |   |   |   |   | 10/30/06 |   |   |   |   | 11/6/06 |   |   |   |   | 11/13/06 |   |   |   |   | 11/20/06 |   |   |   |   | 11/27/06 |   |   |   |   | 12/4/06 |   |   |   |   |   |   |   |   |
|--|---|---|---|---|----------|---|---|---|---|---------|---|---|---|---|----------|---|---|---|---|----------|---|---|---|---|----------|---|---|---|---|---------|---|---|---|---|---|---|---|---|
| T  | W | T | F | S | S        | M | T | W | T | F       | S | S | M | T | W        | T | F | S | S | M        | T | W | T | F | S        | S | M | T | W | T       | F | S | S | M | T | W | T | F |
| roject Manager: NISS III,User Analyst: NISS III,User Analyst: NISS II,User Analyst: NISS I,User Analyst: Pharm D,Outcomes/Reports Analyst: NISS II,Systems Administration: McK Sui |   |   |   |   |          |   |   |   |   |         |   |   |   |   |          |   |   |   |   |          |   |   |   |   |          |   |   |   |   |         |   |   |   |   |   |   |   |   |







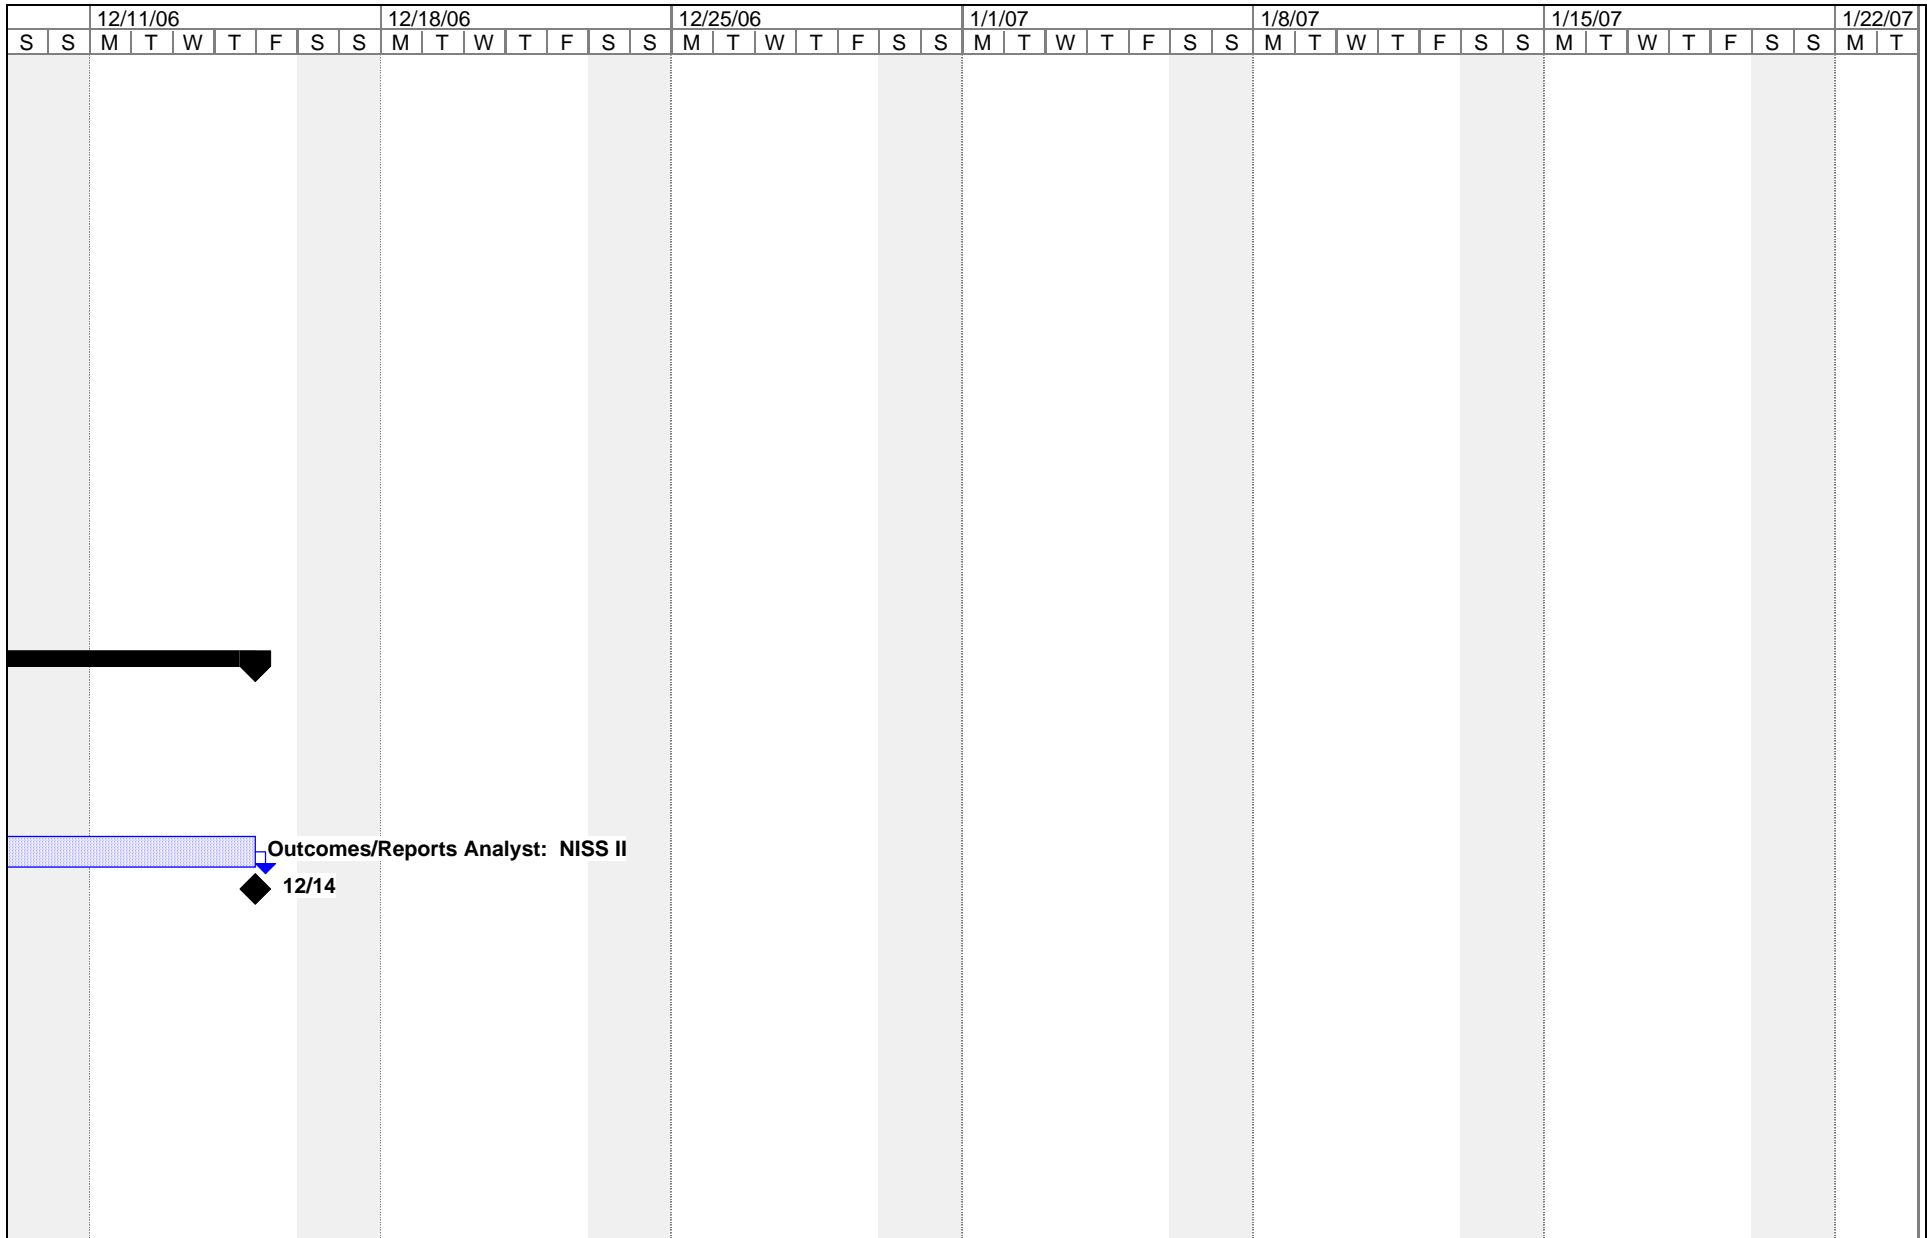


|  |  |   |  |
|--|--|---|--|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task      | Milestone        | External Tasks      |
|  | Split     | Summary          | External Milestone  |
|  | Progress  | Project Summary  | Deadline            |

| 12/11/06 |   | 12/18/06 |   | 12/25/06 |   | 1/1/07 |   | 1/8/07 |   | 1/15/07 |   | 1/22/07 |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
|----------|---|----------|---|----------|---|--------|---|--------|---|---------|---|---------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| S        | S | M        | T | W        | T | F      | S | S      | M | T       | W | T       | F | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S | S | M | T |
|          |   |          |   |          |   |        |   |        |   |         |   |         |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |










Project: Nursing & Patient Care Docun  
Date: Mon 4/10/06

|          |   |                 |   |                    |   |
|----------|---|-----------------|---|--------------------|---|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |












|  |  |   |  |
|--|--|---|--|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task      | Milestone        | External Tasks      |
|  | Split     | Summary          | External Milestone  |
|  | Progress  | Project Summary  | Deadline            |

|   |   | 12/11/06 |   |   |   |   |   |   | 12/18/06 |   |   |   |   |   |   | 12/25/06 |   |   |   |   |   |   | 1/1/07 |   |   |   |   |   |   | 1/8/07 |   |   |   |   |   |   | 1/15/07 |   |   |   |   |   |   | 1/22/07 |   |
|---|---|----------|---|---|---|---|---|---|----------|---|---|---|---|---|---|----------|---|---|---|---|---|---|--------|---|---|---|---|---|---|--------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|
| S | S | M        | T | W | T | F | S | S | M        | T | W | T | F | S | S | M        | T | W | T | F | S | S | M      | T | W | T | F | S | S | M      | T | W | T | F | S | S | M       | T | W | T | F | S | S | M       | T |
|   |   |          |   |   |   |   |   |   |          |   |   |   |   |   |   |          |   |   |   |   |   |   |        |   |   |   |   |   |   |        |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |



|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |

|   |   | 12/11/06 |   |   |   |   |   |   | 12/18/06 |   |   |   |   |   |   | 12/25/06 |   |   |   |   |   |   | 1/1/07 |   |   |   |   |   |   | 1/8/07 |   |   |   |   |   |   | 1/15/07 |   |   |   |   |   |   | 1/22/07 |   |
|---|---|----------|---|---|---|---|---|---|----------|---|---|---|---|---|---|----------|---|---|---|---|---|---|--------|---|---|---|---|---|---|--------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|
| S | S | M        | T | W | T | F | S | S | M        | T | W | T | F | S | S | M        | T | W | T | F | S | S | M      | T | W | T | F | S | S | M      | T | W | T | F | S | S | M       | T | W | T | F | S | S | M       | T |
|   |   |          |   |   |   |   |   |   |          |   |   |   |   |   |   |          |   |   |   |   |   |   |        |   |   |   |   |   |   |        |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |

|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |



|   |   |   |   |   | 1/29/07 |   |   |   |   | 2/5/07 |   |   |   |   | 2/12/07 |   |   |   |   | 2/19/07 |   |   |   |   | 2/26/07 |   |   |   |   | 3/5/07 |   |   |   |   |   |   |   |   |   |
|---|---|---|---|---|---------|---|---|---|---|--------|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|--------|---|---|---|---|---|---|---|---|---|
| W | T | F | S | S | M       | T | W | T | F | S      | S | M | T | W | T       | F | S | S | M | T       | W | T | F | S | S       | M | T | W | T | F      | S | S | M | T | W | T | F | S | S |
|   |   |   |   |   |         |   |   |   |   |        |   |   |   |   |         |   |   |   |   |         |   |   |   |   |         |   |   |   |   |        |   |   |   |   |   |   |   |   |   |

Project: Nursing & Patient Care Docun  
Date: Mon 4/10/06










|          |   |                 |   |                    |   |
|----------|---|-----------------|---|--------------------|---|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |

|   |   |   |   |   | 1/29/07 |   |   |   |   | 2/5/07 |   |   |   |   | 2/12/07 |   |   |   |   | 2/19/07 |   |   |   |   | 2/26/07 |   |   |   |   | 3/5/07 |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
|---|---|---|---|---|---------|---|---|---|---|--------|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|--------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| W | T | F | S | S | M       | T | W | T | F | S      | S | M | T | W | T       | F | S | S | M | T       | W | T | F | S | S       | M | T | W | T | F      | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S |
|   |   |   |   |   |         |   |   |   |   |        |   |   |   |   |         |   |   |   |   |         |   |   |   |   |         |   |   |   |   |        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |

Project: Nursing & Patient Care Docun  
Date: Mon 4/10/06










|          |   |                 |   |                    |   |
|----------|---|-----------------|---|--------------------|---|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |

|   |   |   |   |   | 1/29/07 |   |   |   |   | 2/5/07 |   |   |   |   | 2/12/07 |   |   |   |   | 2/19/07 |   |   |   |   | 2/26/07 |   |   |   |   | 3/5/07 |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
|---|---|---|---|---|---------|---|---|---|---|--------|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|--------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| W | T | F | S | S | M       | T | W | T | F | S      | S | M | T | W | T       | F | S | S | M | T       | W | T | F | S | S       | M | T | W | T | F      | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S |
|   |   |   |   |   |         |   |   |   |   |        |   |   |   |   |         |   |   |   |   |         |   |   |   |   |         |   |   |   |   |        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |

|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |



|   |   |   |   |   | 1/29/07 |   |   |   |   | 2/5/07 |   |   |   |   | 2/12/07 |   |   |   |   | 2/19/07 |   |   |   |   | 2/26/07 |   |   |   |   | 3/5/07 |   |   |   |   |   |   |   |   |   |
|---|---|---|---|---|---------|---|---|---|---|--------|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|--------|---|---|---|---|---|---|---|---|---|
| W | T | F | S | S | M       | T | W | T | F | S      | S | M | T | W | T       | F | S | S | M | T       | W | T | F | S | S       | M | T | W | T | F      | S | S | M | T | W | T | F | S | S |
|   |   |   |   |   |         |   |   |   |   |        |   |   |   |   |         |   |   |   |   |         |   |   |   |   |         |   |   |   |   |        |   |   |   |   |   |   |   |   |   |

|  |
|--|
|  |
|--|










|  |  |   |  |
|--|--|---|--|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task      | Milestone        | External Tasks      |
|  | Split     | Summary          | External Milestone  |
|  | Progress  | Project Summary  | Deadline            |

| 3/12/07 |   |   |   |   |   |   | 3/19/07 |   |   |   |   |   |   | 3/26/07 |   |   |   |   |   |   | 4/2/07 |   |   |   |   |   |   | 4/9/07 |   |   |   |   |   |   | 4/16/07 |   |   |   |   |   |   | 4/23/07 |   |   |   |
|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|--------|---|---|---|---|---|---|--------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|
| S       | M | T | W | T | F | S | S       | M | T | W | T | F | S | S       | M | T | W | T | F | S | S      | M | T | W | T | F | S | S      | M | T | W | T | F | S | S       | M | T | W | T | F | S | S       | M | T | W |
|         |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |   |   |   |        |   |   |   |   |   |   |        |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |










Project: Nursing & Patient Care Docun  
Date: Mon 4/10/06



|          |   |                 |   |                    |   |
|----------|---|-----------------|---|--------------------|---|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |

| 3/12/07 |   |   |   |   |   |   | 3/19/07 |   |   |   |   |   |   | 3/26/07 |   |   |   |   |   |   | 4/2/07 |   |   |   |   |   |   | 4/9/07 |   |   |   |   |   |   | 4/16/07 |   |   |   |   |   |   | 4/23/07 |   |   |   |
|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|--------|---|---|---|---|---|---|--------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|
| S       | M | T | W | T | F | S | S       | M | T | W | T | F | S | S       | M | T | W | T | F | S | S      | M | T | W | T | F | S | S      | M | T | W | T | F | S | S       | M | T | W | T | F | S | S       | M | T | W |
|         |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |   |   |   |        |   |   |   |   |   |   |        |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |

|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |





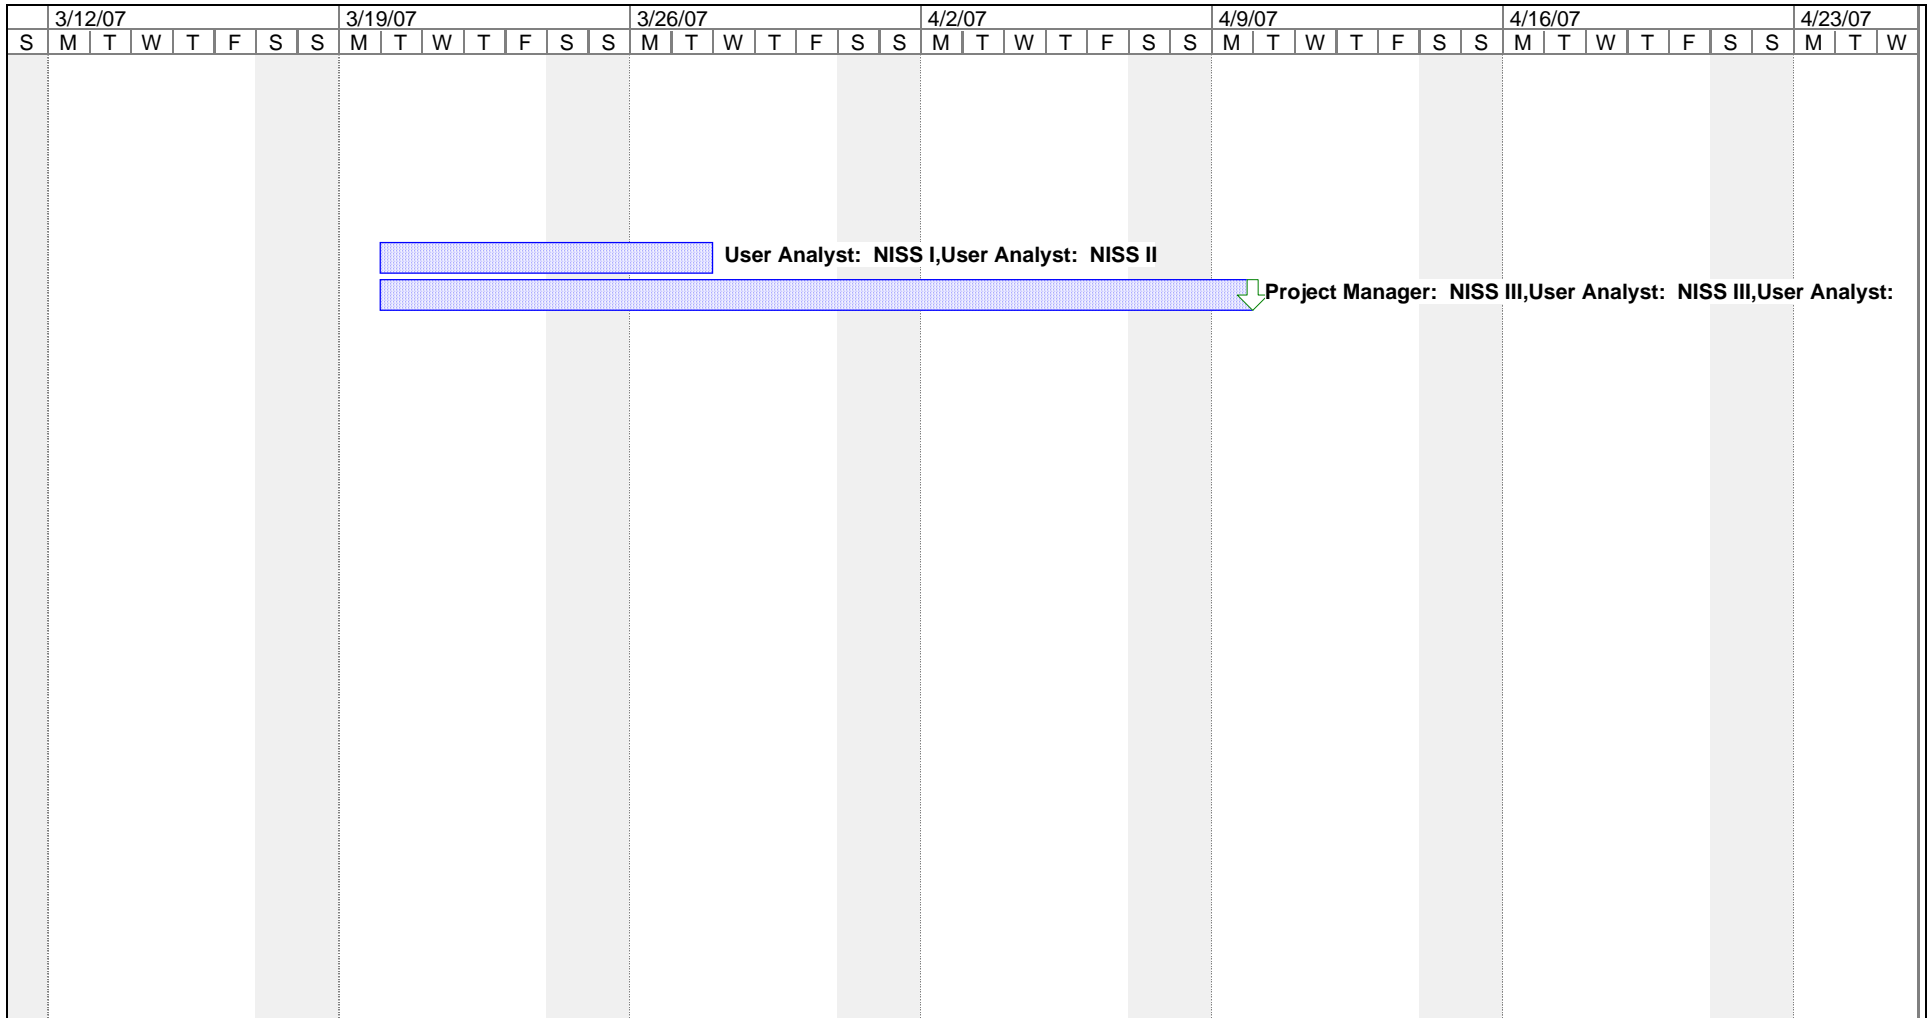




| 3/12/07 |   |   |   |   |   |   | 3/19/07 |   |   |   |   |   |   | 3/26/07 |   |   |   |   |   |   | 4/2/07 |   |   |   |   |   |   | 4/9/07 |   |   |   |   |   |   | 4/16/07 |   |   |   |   |   |   | 4/23/07 |   |   |   |
|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|--------|---|---|---|---|---|---|--------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|
| S       | M | T | W | T | F | S | S       | M | T | W | T | F | S | S       | M | T | W | T | F | S | S      | M | T | W | T | F | S | S      | M | T | W | T | F | S | S       | M | T | W | T | F | S | S       | M | T | W |
|         |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |   |   |   |        |   |   |   |   |   |   |        |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |

|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |



|  |          |  |                 |  |                    |  |
|--|----------|--|-----------------|--|--------------------|--|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |

|   |   |   |   | 4/30/07 |   |   |   | 5/7/07 |   |   |   | 5/14/07 |   |   |   | 5/21/07 |   |   |   | 5/28/07 |   |   |   | 6/4/07 |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
|---|---|---|---|---------|---|---|---|--------|---|---|---|---------|---|---|---|---------|---|---|---|---------|---|---|---|--------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| T | F | S | S | M       | T | W | T | F      | S | S | M | T       | W | T | F | S       | S | M | T | W       | T | F | S | S      | M | T | W | T | F | S | S | M | T | W | T | F | S | S |
|   |   |   |   |         |   |   |   |        |   |   |   |         |   |   |   |         |   |   |   |         |   |   |   |        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |










|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |

|   |   |   |   | 4/30/07 |   |   |   | 5/7/07 |   |   |   | 5/14/07 |   |   |   | 5/21/07 |   |   |   | 5/28/07 |   |   |   | 6/4/07 |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
|---|---|---|---|---------|---|---|---|--------|---|---|---|---------|---|---|---|---------|---|---|---|---------|---|---|---|--------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| T | F | S | S | M       | T | W | T | F      | S | S | M | T       | W | T | F | S       | S | M | T | W       | T | F | S | S      | M | T | W | T | F | S | S | M | T | W | T | F | S | S |
|   |   |   |   |         |   |   |   |        |   |   |   |         |   |   |   |         |   |   |   |         |   |   |   |        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |

Project: Nursing & Patient Care Docun  
Date: Mon 4/10/06










|          |   |                 |   |                    |   |
|----------|---|-----------------|---|--------------------|---|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |

|   |   |   |   | 4/30/07 |   |   |   | 5/7/07 |   |   |   | 5/14/07 |   |   |   | 5/21/07 |   |   |   | 5/28/07 |   |   |   | 6/4/07 |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
|---|---|---|---|---------|---|---|---|--------|---|---|---|---------|---|---|---|---------|---|---|---|---------|---|---|---|--------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| T | F | S | S | M       | T | W | T | F      | S | S | M | T       | W | T | F | S       | S | M | T | W       | T | F | S | S      | M | T | W | T | F | S | S | M | T | W | T | F | S | S |
|   |   |   |   |         |   |   |   |        |   |   |   |         |   |   |   |         |   |   |   |         |   |   |   |        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |

|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |

|  |   |   |   | 4/30/07 |   |   |   | 5/7/07 |   |   |   | 5/14/07 |   |   |   | 5/21/07 |   |   |   | 5/28/07 |   |   |   | 6/4/07 |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
|--|---|---|---|---------|---|---|---|--------|---|---|---|---------|---|---|---|---------|---|---|---|---------|---|---|---|--------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| T  | F | S | S | M       | T | W | T | F      | S | S | M | T       | W | T | F | S       | S | M | T | W       | T | F | S | S      | M | T | W | T | F | S | S | M | T | W | T | F | S | S |
| NISS II,User Analyst: NISS I,User Analyst: Pharm D,Outcomes/Reports Analyst: NISS II,Systems Administration: McK Suite,Desktop Support 1,Desktop Support 2,Help Desk 1,SuperUs |   |   |   |         |   |   |   |        |   |   |   |         |   |   |   |         |   |   |   |         |   |   |   |        |   |   |   |   |   |   |   |   |   |   |   |   |   |   |

Project: Nursing & Patient Care Docun  
Date: Mon 4/10/06










|          |   |                 |   |                    |   |
|----------|---|-----------------|---|--------------------|---|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |

| 6/11/07 |   |   |   |   |   |   | 6/18/07 |   |   |   |   |   |   | 6/25/07 |   |   |   |   |   |   | 7/2/07 |   |   |   |   |   |   | 7/9/07 |   |   |   |   |   |   | 7/16/07 |   |   |   |   |   |   | 7/23/07 |   |   |   |
|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|--------|---|---|---|---|---|---|--------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|
| M       | T | W | T | F | S | S | M       | T | W | T | F | S | S | M       | T | W | T | F | S | S | M      | T | W | T | F | S | S | M      | T | W | T | F | S | S | M       | T | W | T | F | S | S | M       | T | W | T |
|         |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |   |   |   |        |   |   |   |   |   |   |        |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |










Project: Nursing & Patient Care Docun  
Date: Mon 4/10/06

|          |   |                 |   |                    |   |
|----------|---|-----------------|---|--------------------|---|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |

| 6/11/07 |   |   |   |   |   |   | 6/18/07 |   |   |   |   |   |   | 6/25/07 |   |   |   |   |   |   | 7/2/07 |   |   |   |   |   |   | 7/9/07 |   |   |   |   |   |   | 7/16/07 |   |   |   |   |   |   | 7/23/07 |   |   |   |
|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|--------|---|---|---|---|---|---|--------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|
| M       | T | W | T | F | S | S | M       | T | W | T | F | S | S | M       | T | W | T | F | S | S | M      | T | W | T | F | S | S | M      | T | W | T | F | S | S | M       | T | W | T | F | S | S | M       | T | W | T |
|         |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |   |   |   |        |   |   |   |   |   |   |        |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |










|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |


| 6/11/07 |   |   |   |   |   |   | 6/18/07 |   |   |   |   |   |   | 6/25/07 |   |   |   |   |   |   | 7/2/07 |   |   |   |   |   |   | 7/9/07 |   |   |   |   |   |   | 7/16/07 |   |   |   |   |   |   | 7/23/07 |   |   |   |  |  |  |
|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|--------|---|---|---|---|---|---|--------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|--|--|--|
| M       | T | W | T | F | S | S | M       | T | W | T | F | S | S | M       | T | W | T | F | S | S | M      | T | W | T | F | S | S | M      | T | W | T | F | S | S | M       | T | W | T | F | S | S | M       | T | W | T |  |  |  |
|         |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |   |   |   |        |   |   |   |   |   |   |        |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |  |  |  |

|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |

| 6/11/07                                     |   |   |   |   |   |   | 6/18/07 |   |   |   |   |   |   | 6/25/07 |   |   |   |   |   |   | 7/2/07 |   |   |   |   |   |   | 7/9/07 |   |   |   |   |   |   | 7/16/07 |   |   |   |   |   |   | 7/23/07 |   |   |   |  |  |  |
|---|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|--------|---|---|---|---|---|---|--------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|--|--|--|
| M   | T | W | T | F | S | S | M       | T | W | T | F | S | S | M       | T | W | T | F | S | S | M      | T | W | T | F | S | S | M      | T | W | T | F | S | S | M       | T | W | T | F | S | S | M       | T | W | T |  |  |  |
| User Analyst: NISS I, User Analyst: NISS II |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |   |   |   |        |   |   |   |   |   |   |        |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |  |  |  |

Project: Nursing & Patient Care Docun  
Date: Mon 4/10/06

|          |   |                 |   |                    |   |
|----------|---|-----------------|---|--------------------|---|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |

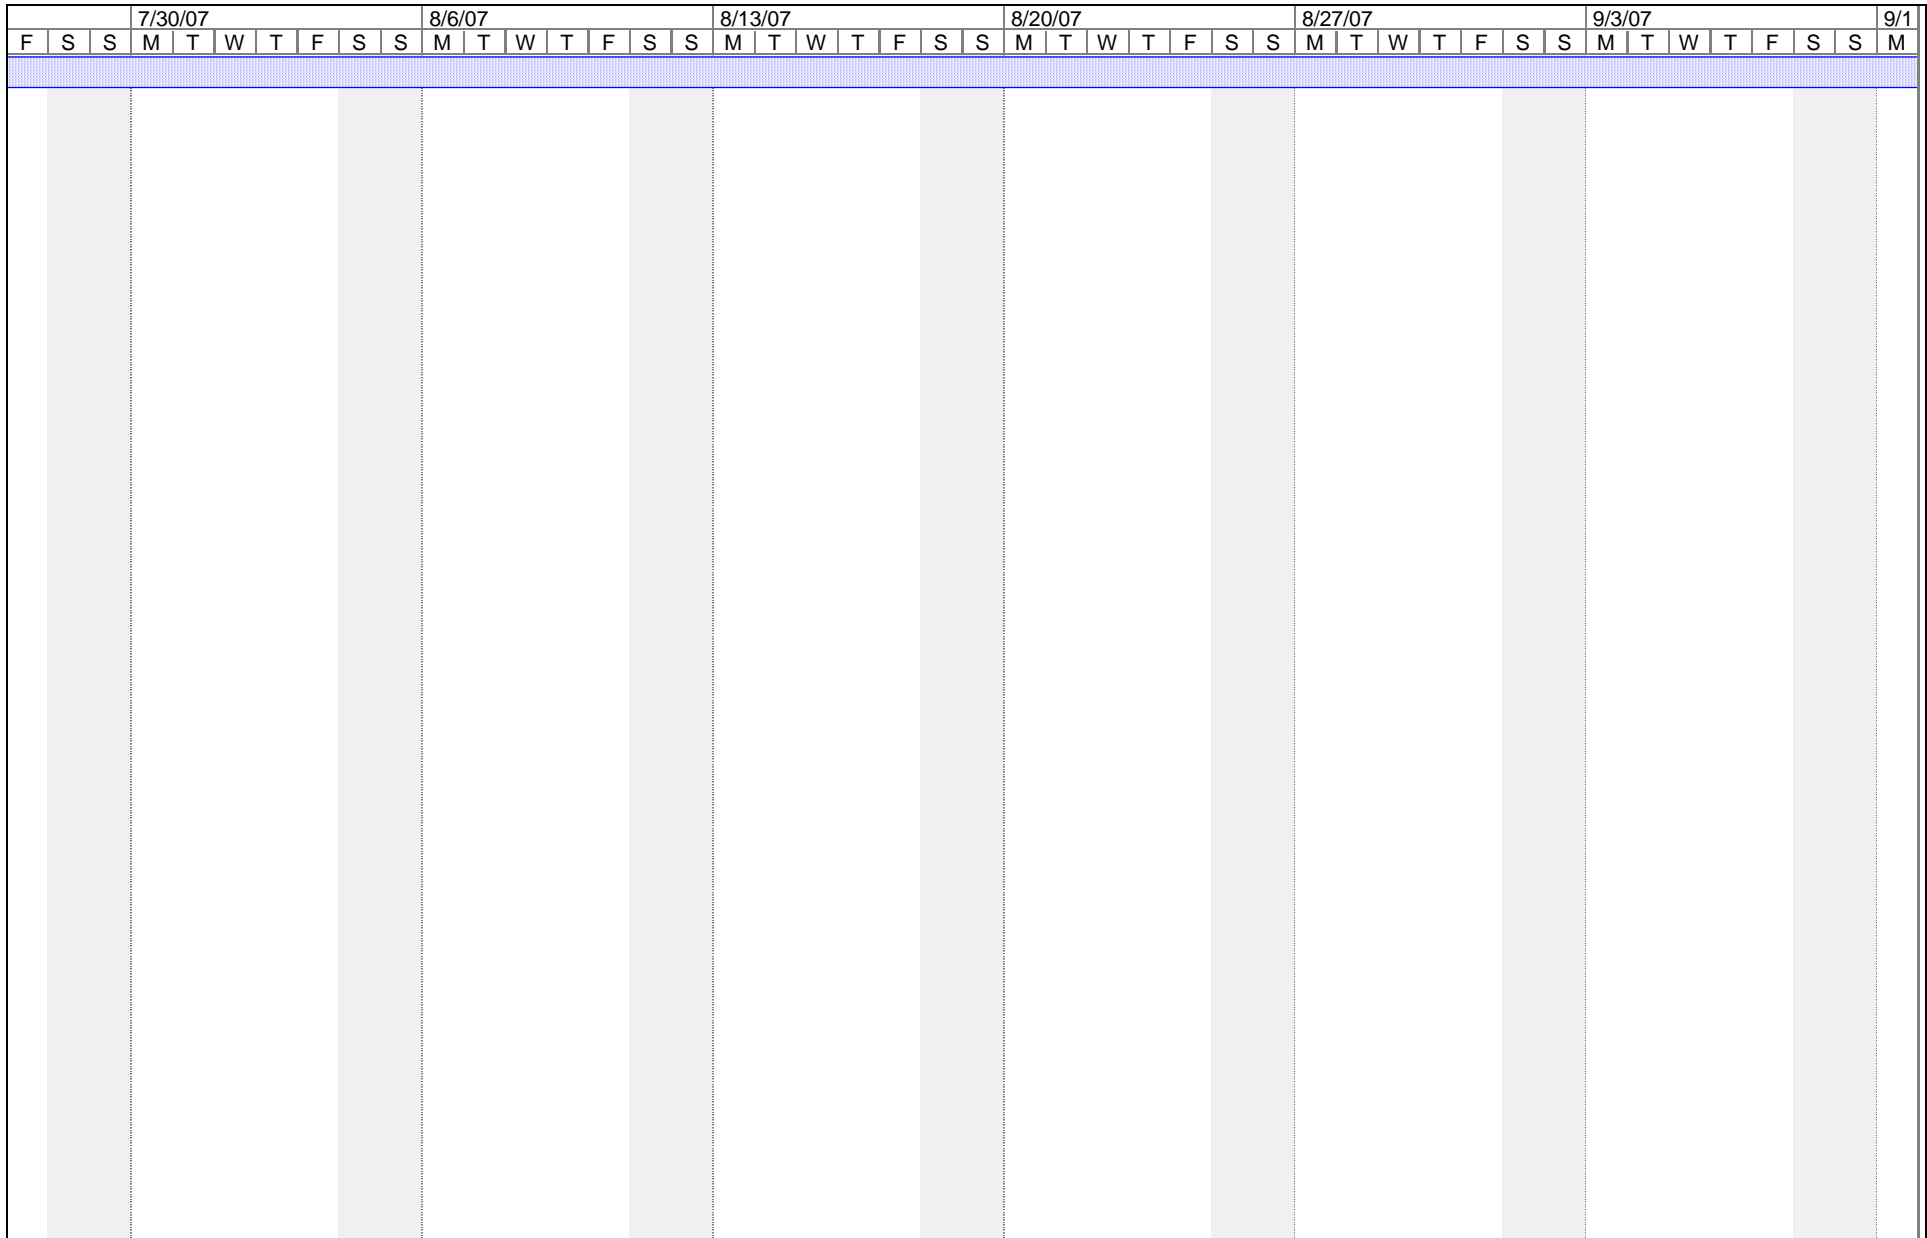

Project: Nursing & Patient Care Docun  
 Date: Mon 4/10/06










|          |   |                 |   |                    |   |
|----------|---|-----------------|---|--------------------|---|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |


| 7/30/07 |   |   | 8/6/07 |   |   |   |   | 8/13/07 |   |   |   |   | 8/20/07 |   |   |   |   | 8/27/07 |   |   |   |   | 9/3/07 |   |   |   |   | 9/1 |   |   |   |   |   |   |   |   |   |   |
|---------|---|---|--------|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|--------|---|---|---|---|-----|---|---|---|---|---|---|---|---|---|---|
| F       | S | S | M      | T | W | T | F | S       | S | M | T | W | T       | F | S | S | M | T       | W | T | F | S | S      | M | T | W | T | F   | S | S | M | T | W | T | F | S | S | M |
|         |   |   |        |   |   |   |   |         |   |   |   |   |         |   |   |   |   |         |   |   |   |   |        |   |   |   |   |     |   |   |   |   |   |   |   |   |   |   |

Project: Nursing & Patient Care Docun  
Date: Mon 4/10/06


|          |   |                 |   |                    |   |
|----------|---|-----------------|---|--------------------|---|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |

| 7/30/07 |   |   | 8/6/07 |   |   |   |   | 8/13/07 |   |   |   |   | 8/20/07 |   |   |   |   | 8/27/07 |   |   |   |   | 9/3/07 |   |   |   |   | 9/1 |   |   |   |   |   |   |   |   |   |   |
|---------|---|---|--------|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|--------|---|---|---|---|-----|---|---|---|---|---|---|---|---|---|---|
| F       | S | S | M      | T | W | T | F | S       | S | M | T | W | T       | F | S | S | M | T       | W | T | F | S | S      | M | T | W | T | F   | S | S | M | T | W | T | F | S | S | M |
|         |   |   |        |   |   |   |   |         |   |   |   |   |         |   |   |   |   |         |   |   |   |   |        |   |   |   |   |     |   |   |   |   |   |   |   |   |   |   |

|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |

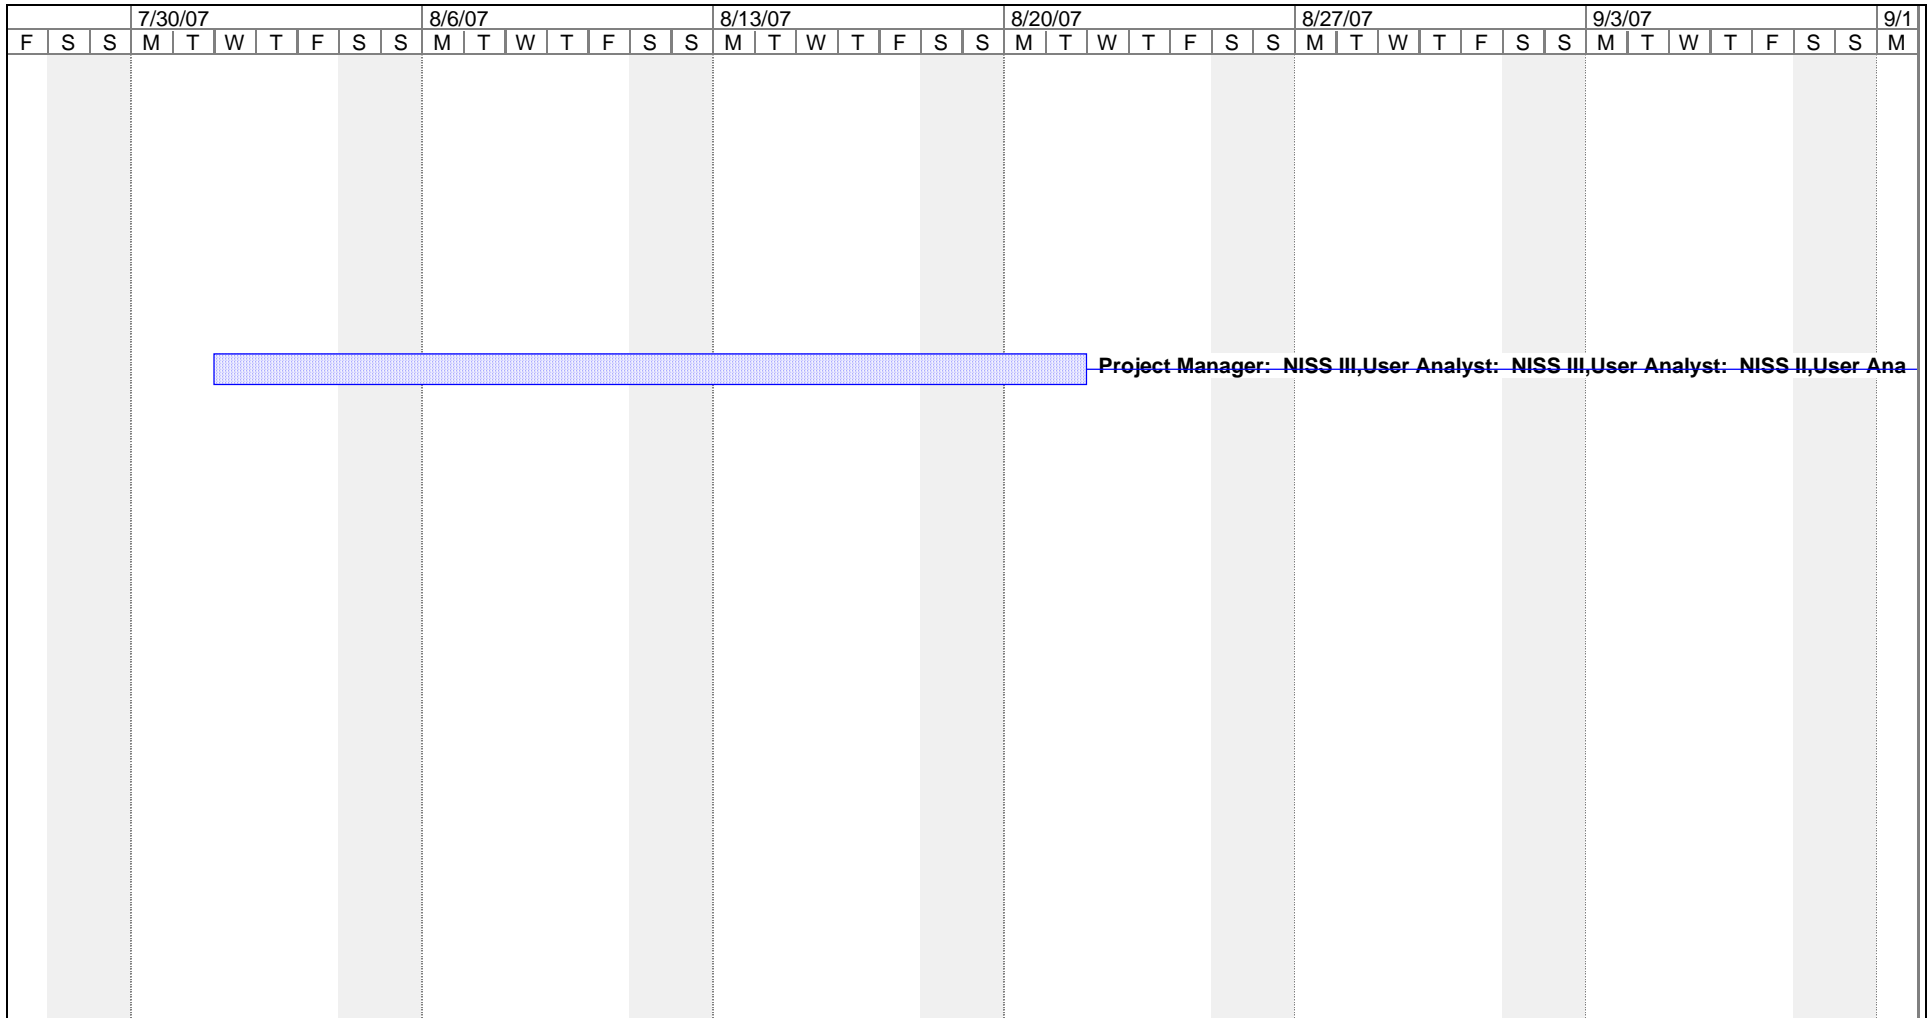

Project: Nursing & Patient Care Docun  
Date: Mon 4/10/06

|          |   |                 |   |                    |   |
|----------|---|-----------------|---|--------------------|---|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |



| /07 |   |   |   |   |   | 9/17/07 |   |   |   |   |   | 9/24/07 |   |   |   |   |   | 10/1/07 |   |   |   |   |   | 10/8/07 |   |   |   |   |   | 10/15/07 |   |   |   |   |   | 10/22/07 |   |   |   |   |   |   |   |   |   |
|-----|---|---|---|---|---|---------|---|---|---|---|---|---------|---|---|---|---|---|---------|---|---|---|---|---|---------|---|---|---|---|---|----------|---|---|---|---|---|----------|---|---|---|---|---|---|---|---|---|
| T   | W | T | F | S | S | M       | T | W | T | F | S | S       | M | T | W | T | F | S       | S | M | T | W | T | F       | S | S | M | T | W | T        | F | S | S | M | T | W        | T | F | S | S | M | T | W | T | F |
|     |   |   |   |   |   |         |   |   |   |   |   |         |   |   |   |   |   |         |   |   |   |   |   |         |   |   |   |   |   |          |   |   |   |   |   |          |   |   |   |   |   |   |   |   |   |

Project: Nursing & Patient Care Docun  
Date: Mon 4/10/06

|          |   |                 |   |                    |   |
|----------|---|-----------------|---|--------------------|---|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |





| /07 |   | 9/17/07 |   | 9/24/07 |   | 10/1/07 |   | 10/8/07 |   | 10/15/07 |   | 10/22/07 |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
|-----|---|---------|---|---------|---|---------|---|---------|---|----------|---|----------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| T   | W | T       | F | S       | S | M       | T | W       | T | F        | S | S        | M | T | W | T | F | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S | S |
|     |   |         |   |         |   |         |   |         |   |          |   |          |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |

Project: Nursing & Patient Care Docun  
Date: Mon 4/10/06

|          |   |                 |   |                    |   |
|----------|---|-----------------|---|--------------------|---|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |

| /07  |   | 9/17/07 |   | 9/24/07 |   | 10/1/07 |   | 10/8/07 |   | 10/15/07 |   | 10/22/07 |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
|--|---|---------|---|---------|---|---------|---|---------|---|----------|---|----------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| T  | W | T       | F | S       | S | M       | T | W       | T | F        | S | S        | M | T | W | T | F | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S | S |
| <del>lyst: NISS I,User Analyst: Pharm D,Outcomes/Reports Analyst: NISS II,Systems Administration: Mck Suite,Desktop Support 1,Desktop Support 2,Help Desk 1,SuperUsers</del> |   |         |   |         |   |         |   |         |   |          |   |          |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |

Project: Nursing & Patient Care Docun  
Date: Mon 4/10/06










|          |   |                 |   |                    |   |
|----------|---|-----------------|---|--------------------|---|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |

| 10/29/07 |   | 11/5/07 |   | 11/12/07 |   | 11/19/07 |   | 11/26/07 |   | 12/3/07 |   | 12/10/07 |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
|----------|---|---------|---|----------|---|----------|---|----------|---|---------|---|----------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| S        | S | M       | T | W        | T | F        | S | S        | M | T       | W | T        | F | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S | S | M | T |
|          |   |         |   |          |   |          |   |          |   |         |   |          |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |










Project: Nursing & Patient Care Docun  
Date: Mon 4/10/06

|          |   |                 |   |                    |   |
|----------|---|-----------------|---|--------------------|---|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |

|   |   | 10/29/07 |   |   |   |   |   |   | 11/5/07 |   |   |   |   |   |   | 11/12/07 |   |   |   |   |   |   | 11/19/07 |   |   |   |   |   |   | 11/26/07 |   |   |   |   |   |   | 12/3/07 |   |   |   |   |   |   | 12/10/07 |   |
|---|---|----------|---|---|---|---|---|---|---------|---|---|---|---|---|---|----------|---|---|---|---|---|---|----------|---|---|---|---|---|---|----------|---|---|---|---|---|---|---------|---|---|---|---|---|---|----------|---|
| S | S | M        | T | W | T | F | S | S | M       | T | W | T | F | S | S | M        | T | W | T | F | S | S | M        | T | W | T | F | S | S | M        | T | W | T | F | S | S | M       | T | W | T | F | S | S | M        | T |
|   |   |          |   |   |   |   |   |   |         |   |   |   |   |   |   |          |   |   |   |   |   |   |          |   |   |   |   |   |   |          |   |   |   |   |   |   |         |   |   |   |   |   |   |          |   |










|  |  |   |  |
|--|--|---|--|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task      | Milestone        | External Tasks      |
|  | Split     | Summary          | External Milestone  |
|  | Progress  | Project Summary  | Deadline            |

|   |   | 10/29/07 |   |   |   |   |   |   | 11/5/07 |   |   |   |   |   |   | 11/12/07 |   |   |   |   |   |   | 11/19/07 |   |   |   |   |   |   | 11/26/07 |   |   |   |   |   |   | 12/3/07 |   |   |   |   |   |   | 12/10/07 |   |
|---|---|----------|---|---|---|---|---|---|---------|---|---|---|---|---|---|----------|---|---|---|---|---|---|----------|---|---|---|---|---|---|----------|---|---|---|---|---|---|---------|---|---|---|---|---|---|----------|---|
| S | S | M        | T | W | T | F | S | S | M       | T | W | T | F | S | S | M        | T | W | T | F | S | S | M        | T | W | T | F | S | S | M        | T | W | T | F | S | S | M       | T | W | T | F | S | S | M        | T |
|   |   |          |   |   |   |   |   |   |         |   |   |   |   |   |   |          |   |   |   |   |   |   |          |   |   |   |   |   |   |          |   |   |   |   |   |   |         |   |   |   |   |   |   |          |   |

|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |

|   |   | 10/29/07 |   |   |   |   |   |   | 11/5/07 |   |   |   |   |   |   | 11/12/07 |   |   |   |   |   |   | 11/19/07 |   |   |   |   |   |   | 11/26/07 |   |   |   |   |   |   | 12/3/07 |   |   |   |   |   |   | 12/10/0 |   |
|---|---|----------|---|---|---|---|---|---|---------|---|---|---|---|---|---|----------|---|---|---|---|---|---|----------|---|---|---|---|---|---|----------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|
| S | S | M        | T | W | T | F | S | S | M       | T | W | T | F | S | S | M        | T | W | T | F | S | S | M        | T | W | T | F | S | S | M        | T | W | T | F | S | S | M       | T | W | T | F | S | S | M       | T |
|   |   |          |   |   |   |   |   |   |         |   |   |   |   |   |   |          |   |   |   |   |   |   |          |   |   |   |   |   |   |          |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |

|  |  |
|--|--|
|  |  |
|--|--|

|  |   |   |  |
|--|---|---|--|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task <br>Split <br>Progress  | Milestone <br>Summary <br>Project Summary  | External Tasks <br>External Milestone <br>Deadline  |
|--|---|---|--|



|   |   |   |   |   | 12/17/07 |   |   |   |   | 12/24/07 |   |   |   |   | 12/31/07 |   |   |   |   | 1/7/08 |   |   |   |   | 1/14/08 |   |   |   |   | 1/21/08 |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |
|---|---|---|---|---|----------|---|---|---|---|----------|---|---|---|---|----------|---|---|---|---|--------|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| W | T | F | S | S | M        | T | W | T | F | S        | S | M | T | W | T        | F | S | S | M | T      | W | T | F | S | S       | M | T | W | T | F       | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S |
|   |   |   |   |   |          |   |   |   |   |          |   |   |   |   |          |   |   |   |   |        |   |   |   |   |         |   |   |   |   |         |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |


Project: Nursing & Patient Care Docun  
Date: Mon 4/10/06

|          |   |                 |   |                    |   |
|----------|---|-----------------|---|--------------------|---|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |




|   |   |   |   |   | 12/17/07 |   |   |   |   | 12/24/07 |   |   |   |   | 12/31/07 |   |   |   |   | 1/7/08 |   |   |   |   | 1/14/08 |   |   |   |   | 1/21/08 |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |
|---|---|---|---|---|----------|---|---|---|---|----------|---|---|---|---|----------|---|---|---|---|--------|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|--|--|--|--|--|--|--|--|
| W | T | F | S | S | M        | T | W | T | F | S        | S | M | T | W | T        | F | S | S | M | T      | W | T | F | S | S       | M | T | W | T | F       | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S |  |  |  |  |  |  |  |  |
|   |   |   |   |   |          |   |   |   |   |          |   |   |   |   |          |   |   |   |   |        |   |   |   |   |         |   |   |   |   |         |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |

Project: Nursing & Patient Care Docun  
Date: Mon 4/10/06
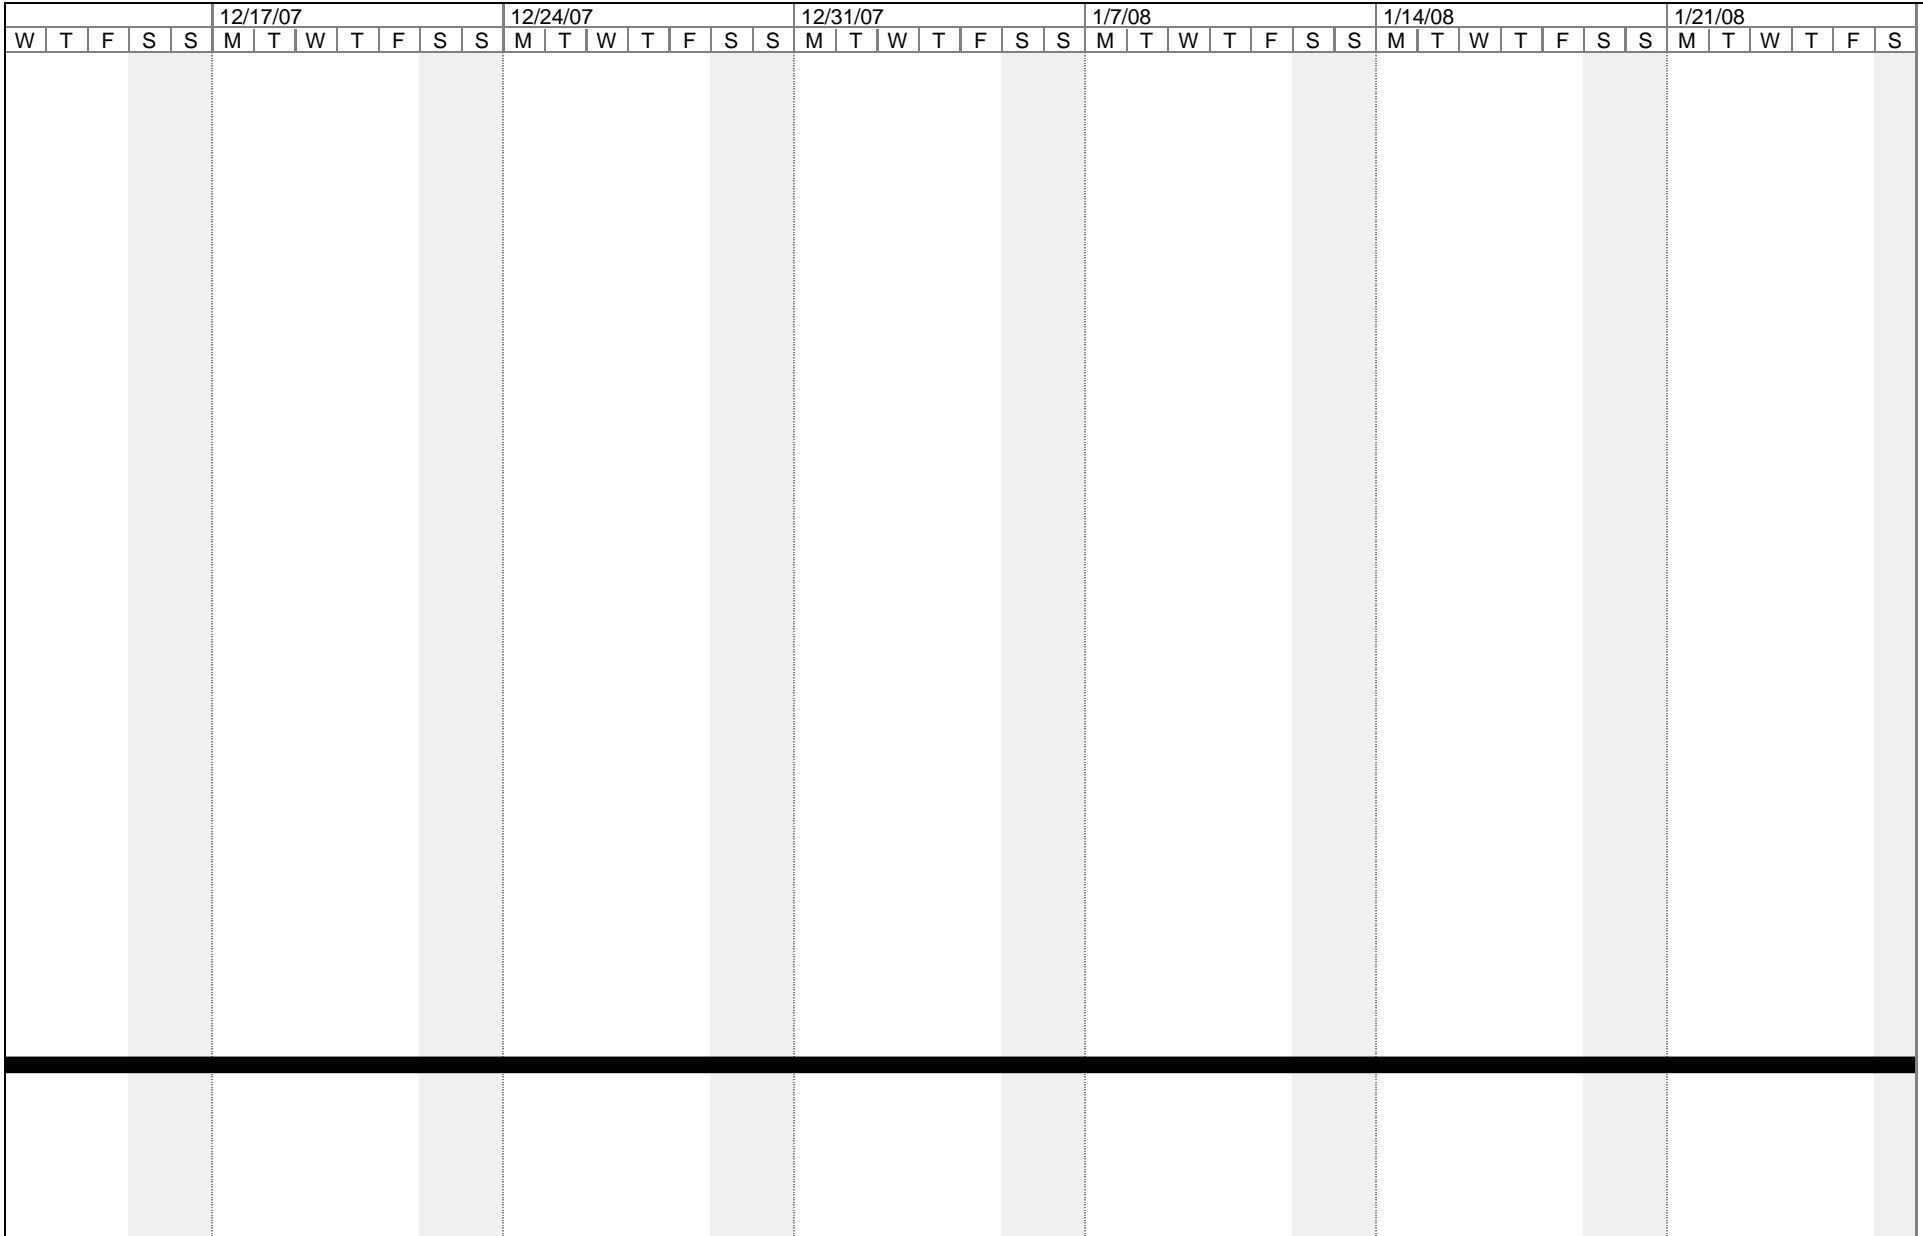
|          |   |                 |   |                    |   |
|----------|---|-----------------|---|--------------------|---|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |












Project: Nursing & Patient Care Docun  
 Date: Mon 4/10/06










|          |   |                 |   |                    |   |
|----------|---|-----------------|---|--------------------|---|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |

|   |   |   |   |   | 12/17/07 |   |   |   |   | 12/24/07 |   |   |   |   | 12/31/07 |   |   |   |   | 1/7/08 |   |   |   |   | 1/14/08 |   |   |   |   | 1/21/08 |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |
|---|---|---|---|---|----------|---|---|---|---|----------|---|---|---|---|----------|---|---|---|---|--------|---|---|---|---|---------|---|---|---|---|---------|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|--|--|--|--|--|--|--|--|
| W | T | F | S | S | M        | T | W | T | F | S        | S | M | T | W | T        | F | S | S | M | T      | W | T | F | S | S       | M | T | W | T | F       | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S |  |  |  |  |  |  |  |  |
|   |   |   |   |   |          |   |   |   |   |          |   |   |   |   |          |   |   |   |   |        |   |   |   |   |         |   |   |   |   |         |   |   |   |   |   |   |   |   |   |   |   |   |   |   |   |  |  |  |  |  |  |  |  |










|  |
|--|
|  |
|--|

|  |  |   |  |
|--|--|---|--|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task      | Milestone        | External Tasks      |
|  | Split     | Summary          | External Milestone  |
|  | Progress  | Project Summary  | Deadline            |


| 1/28/08 |   |   |   |   |   |   | 2/4/08 |   |   |   |   |   |   | 2/11/08 |   |   |   |   |   |   | 2/18/08 |   |   |   |   |   |   | 2/25/08 |   |   |   |   |   |   | 3/3/08 |   |   |   |  |  |  | 3/10/08 |  |  |  |
|---------|---|---|---|---|---|---|--------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|--------|---|---|---|--|--|--|---------|--|--|--|
| S       | M | T | W | T | F | S | S      | M | T | W | T | F | S | S       | M | T | W | T | F | S | S       | M | T | W | T | F | S | S       | M | T | W | T | F | S | S      | M | T | W |  |  |  |         |  |  |  |
|         |   |   |   |   |   |   |        |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |   |   |   |        |   |   |   |  |  |  |         |  |  |  |

|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |

| 1/28/08 |   |   |   |   |   |   | 2/4/08 |   |   |   |   |   |   | 2/11/08 |   |   |   |   |   |   | 2/18/08 |   |   |   |   |   |   | 2/25/08 |   |   |   |   |   |   | 3/3/08 |   |   |   |   |   |   | 3/10/08 |   |   |   |  |
|---------|---|---|---|---|---|---|--------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|---------|---|---|---|---|---|---|--------|---|---|---|---|---|---|---------|---|---|---|--|
| S       | M | T | W | T | F | S | S      | M | T | W | T | F | S | S       | M | T | W | T | F | S | S       | M | T | W | T | F | S | S       | M | T | W | T | F | S | S      | M | T | W | T | F | S | S       | M | T | W |  |
|         |   |   |   |   |   |   |        |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |   |   |   |         |   |   |   |   |   |   |        |   |   |   |   |   |   |         |   |   |   |  |

|  |          |   |                 |   |                    |   |
|--|----------|---|-----------------|---|--------------------|---|
| Project: Nursing & Patient Care Docun<br>Date: Mon 4/10/06 | Task     |  | Milestone       |  | External Tasks     |  |
|  | Split    |  | Summary         |  | External Milestone |  |
|  | Progress |  | Project Summary |  | Deadline           |  |



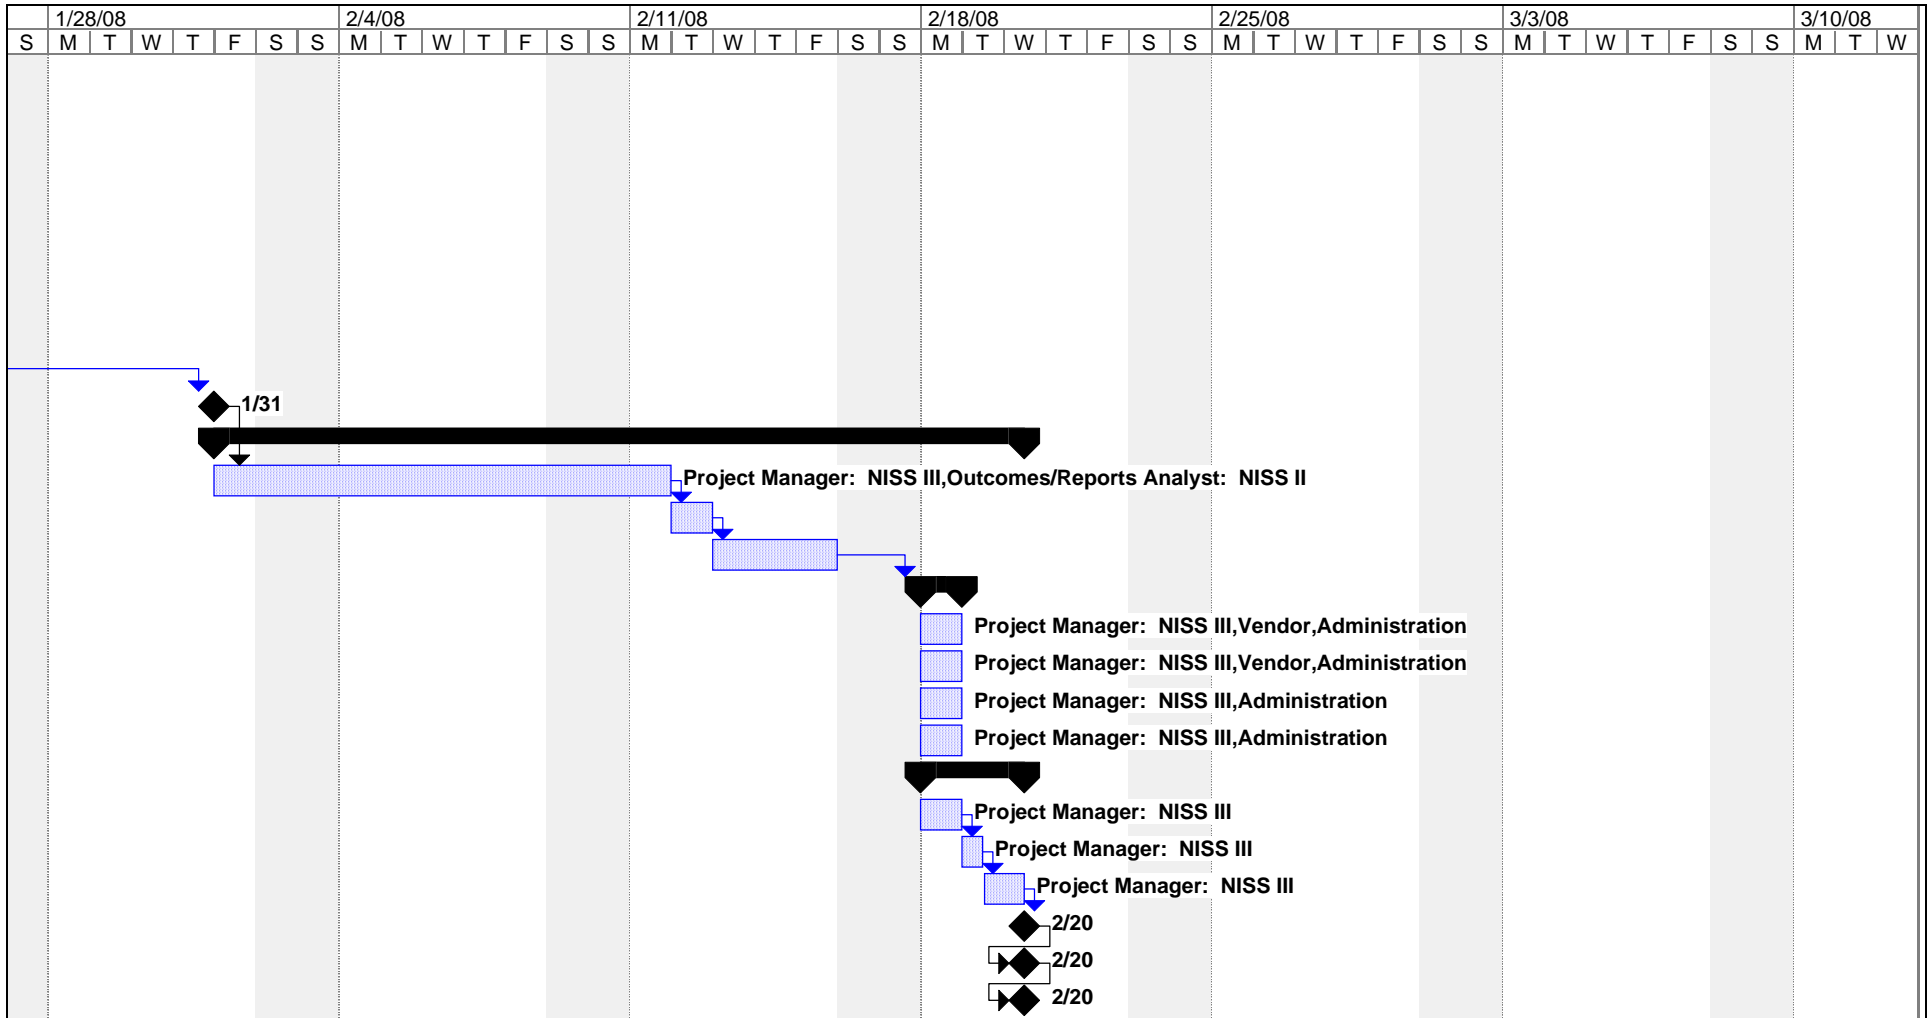

Project: Nursing & Patient Care Docun  
 Date: Mon 4/10/06

|          |  |                 |  |                    |  |
|----------|--|-----------------|--|--------------------|--|
| Task     |  | Milestone       |  | External Tasks     |  |
| Split    |  | Summary         |  | External Milestone |  |
| Progress |  | Project Summary |  | Deadline           |  |
