








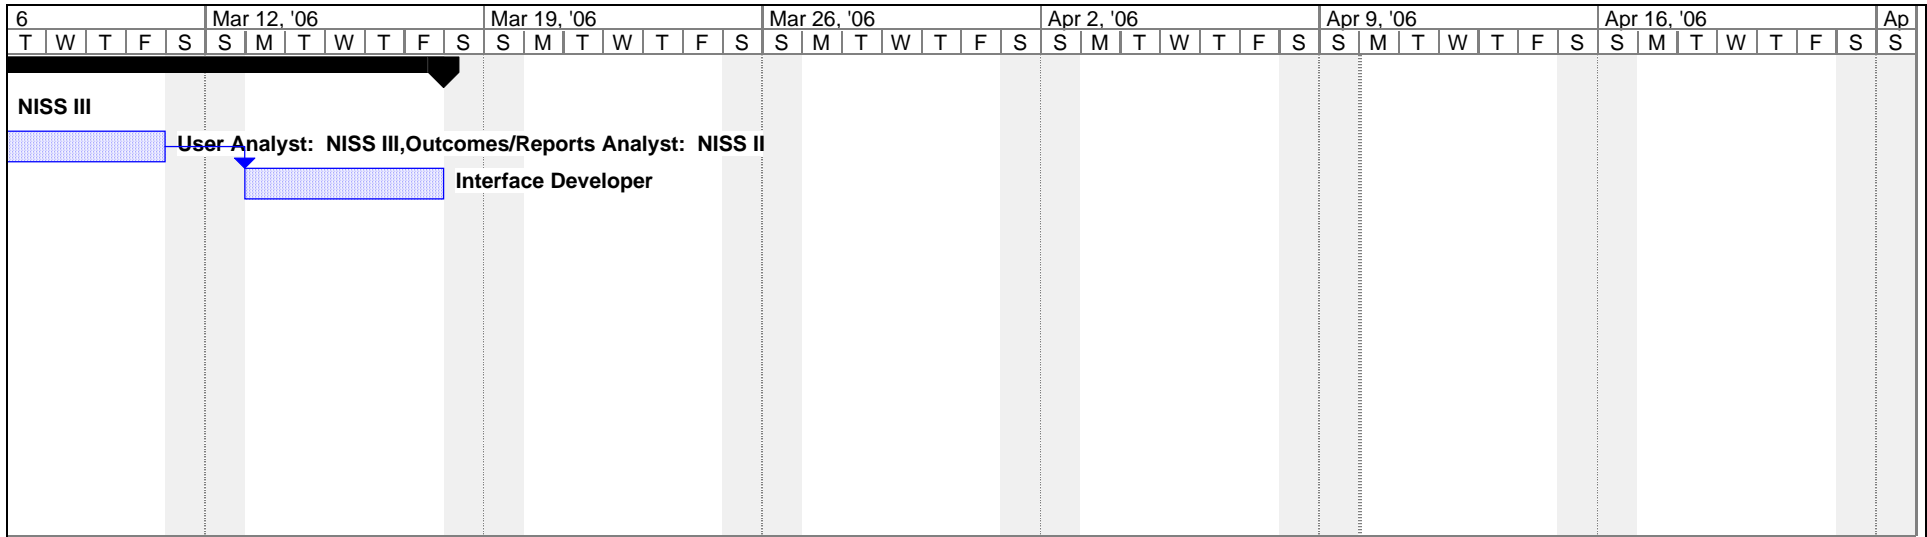











ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	'06							Mar 5, '06
							T	W	T	F	S	S	M	
1	<b>Nursing &amp; Patient Care Documentation System Unit Imple</b>	<b>13 days</b>	<b>Wed 3/1/06</b>	<b>Fri 3/17/06</b>										
2	Announce Project Kickoff	1 day	Wed 3/1/06	Wed 3/1/06		Project Manager: NIS								
3	Conduct needs analysis	5 days	Mon 3/6/06	Fri 3/10/06		User Analyst: NISS III								
4	Incorporate feedback on software specifications	5 days	Mon 3/13/06	Fri 3/17/06	3	Interface Developer								
5	<b>Meet with Nurse Manager to coordinate implementation p</b>	<b>32.75 days</b>	<b>Fri 9/1/06</b>	<b>Tue 10/17/06</b>		<b>User Analyst: NISS I</b>								
6	Determine final deployment strategy	2 days	Fri 9/1/06	Mon 9/4/06		Project Manager: NIS								
7	Install Hardware on target unit(s)	5 days	Tue 9/5/06	Mon 9/11/06		User Analyst: NISS III								
8	Install software on target unit(s)	3 days	Tue 9/12/06	Thu 9/14/06	7	User Analyst: NISS II								
9	Test Software/Hardware once installed	2 days	Fri 9/15/06	Mon 9/18/06	8	User Analyst: NISS II								
10	Train Phase 1 Clinicians/HUC's	5 days	Tue 9/19/06	Mon 9/25/06	9	User Analyst: NISS I,I								
11	Software Go-Live- Phase 1	15 days	Tue 9/26/06	Mon 10/16/06	10	Project Manager: NIS								
12	Phase Implementation Evaluation	6 hrs	Tue 10/17/06	Tue 10/17/06	11	Project Manager: NIS								
13	Software Support Ongoing	0 days	Tue 10/17/06	Tue 10/17/06	12	Help Desk 1,Desktop :								

Project Manager:










Project: Unit specific implementation d Date: Mon 4/10/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: Unit specific implementation d Date: Mon 4/10/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	










23, '06							Apr 30, '06							May 7, '06							May 14, '06							May 21, '06							May 28, '06							Jun 4, '06												
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S							




Project: Unit specific implementation d Date: Mon 4/10/06	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 


Jun 11, '06							Jun 18, '06							Jun 25, '06							Jul 2, '06							Jul 9, '06							Jul 16, '06							Jul 23, '06													
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S							



Project: Unit specific implementation d Date: Mon 4/10/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

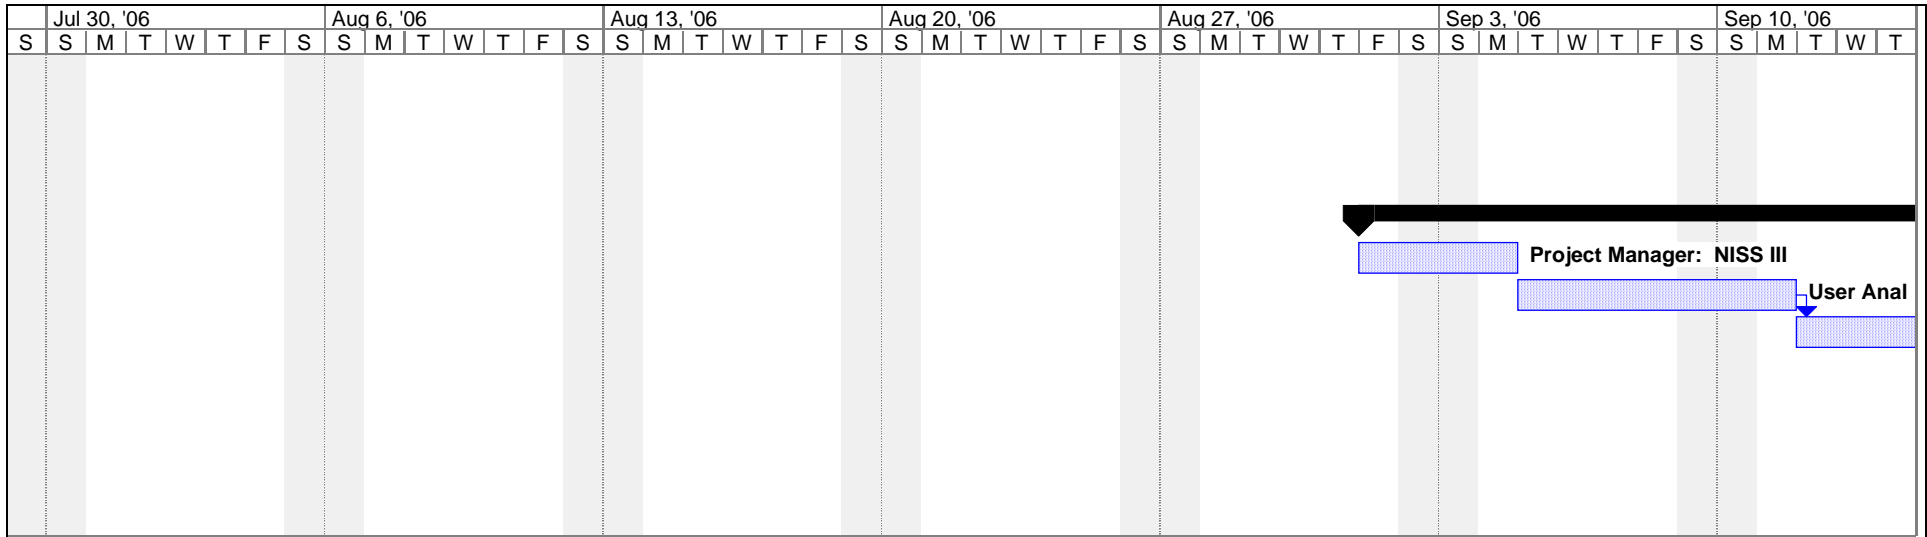



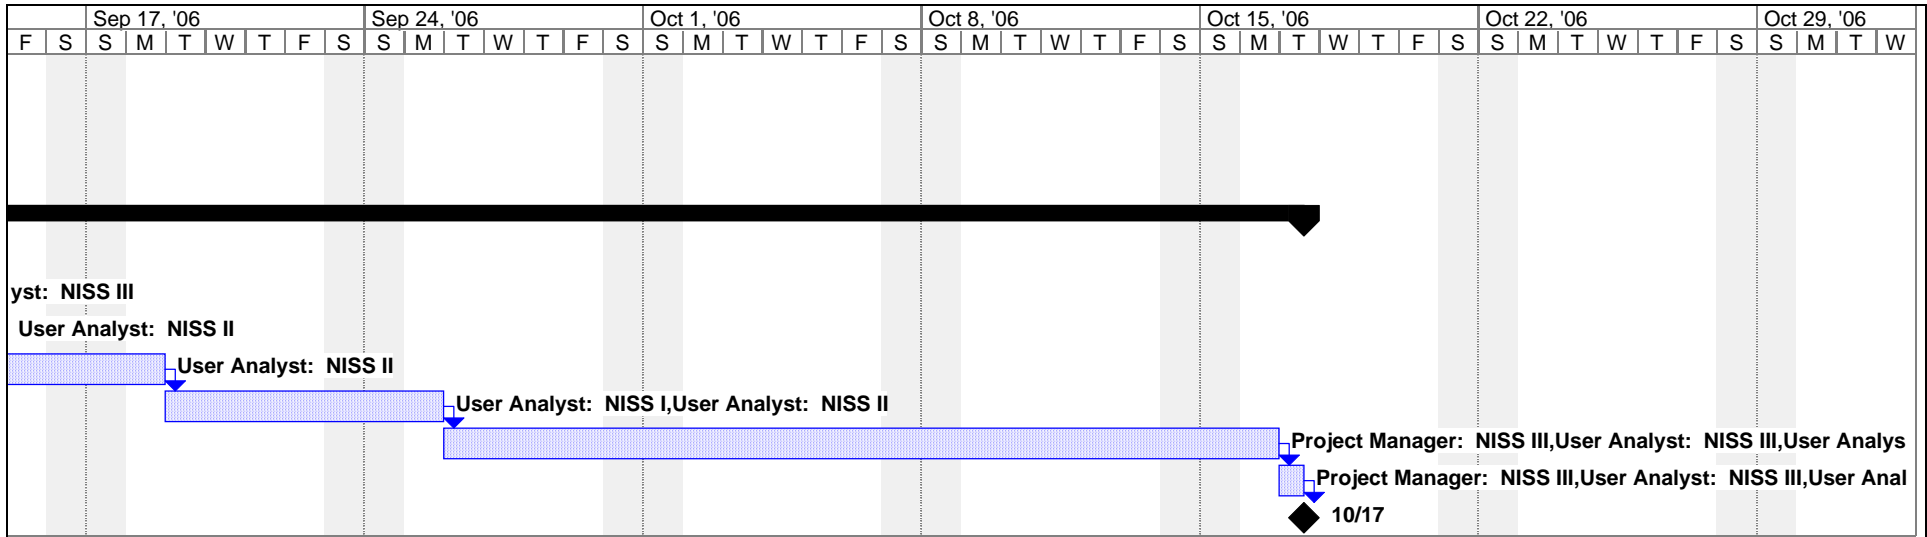





Project: Unit specific implementation d Date: Mon 4/10/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: Unit specific implementation d  
Date: Mon 4/10/06

- Task Milestone
- Split Summary
- Progress Project Summary
- External Tasks
- External Milestone
- Deadline

			Nov 5, '06							Nov 12, '06							Nov 19, '06							Nov 26, '06							Dec 3, '06							Dec 10, '06							Dec 17, '06		
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T
<p>t: NISS II,User Analyst: NISS I,User Analyst: Pharm D,Outcomes/Reports Analyst: NISS II,Systems Administration: McK Suite,Desktop Support 1,Desktop Support 2,Help Desk 1,Super  lyst: NISS II,User Analyst: NISS I,User Analyst: Pharm D,Outcomes/Reports Analyst: NISS II,Systems Administration: McK Suite,Desktop Support 1,Desktop Support 2,Help Desk 1,Su</p>																																															

Project: Unit specific implementation d Date: Mon 4/10/06	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 
